Torres Rojas, Genara FOI #14827

From: dsahler@wcpclaw.com
Sent: Monday, April 07, 2014 3:26 PM
To: Duffy, Daniel
Cc: Torres Rojas, Genara; Van Duyne, Sheree; American, Heavyn-Leigh
Subject: Freedom of Information Online Request Form

Information:

First Name: debra
Last Name: sahler
Company: wildenhain crino
Mailing Address 1: 95 mt. bethel road
Mailing Address 2:
City: warren
State: NJ
Zip Code: 07446
Email Address: dsahler@wcpclaw.com
Phone: 9087573900
Required copies of the records: Yes

List of specific record(s):
Please provide copies of any daily narratives andor daily reports for the project EW-154.028-EWR Rehab of Parking LotP6 for the period of June 1, 2012 thru June 30, 2012 as well as all reports andor daily narratives of any inspector for this project.

THE PORT AUTHORITY OF NY & NJ

FOI Administrator

April 21, 2014

Ms. Debra Sahler
Wildenhain Crino
95 Mt. Bethel Road
Warren, NJ 07446

Re: Freedom of Information Reference No. 14827

Dear Ms. Sahler:

This is in response to your April 7, 2014 request, which has been processed under the Port Authority's Freedom of Information Code (the "Code", copy attached), for "copies of any daily narratives andor daily reports for the project EW-154.028-EWR Rehab of Parking LotP6 for the period of June 1, 2012 thru June 30, 2012 as well as all reports andor daily narratives of any inspector for this project."

Material responsive to your request and available under the Code can be found on the Port Authority's website at http://www.panynj.gov/corporate-information/foi/14827-C.pdf. Paper copies of the available records are available upon request.

Please refer to the above FOI reference number in any future correspondence relating to your request.

Very truly yours,

Daniel D. Duffy
FOI Administrator

Attachment

225 Park Avenue South, 17th Floor
New York, NY 10003
T: 212 435 3642
F: 212 435 7555

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, N.J. 07203

FOREMAN:

WEEK ENDING 6/16/12

DATE	6/11/12			6/12/12			6/13/12			6/14/12			6/15/12		
DAY	MONDAY			TUESDAY			WEDNESDAY			THURSDAY			FRIDAY		
JOB NO	BLL 121			4218 / BLL 121						BLL # 121			BLL # 121		
DESCRIPTION	Tractor Trailer BLL # 121 Teterboro			Dump Truck & Tractor Trailer			Dump Truck & Tractor Trailer			Dump Truck			Tractor Trailer		
EMPLOYEE	no lunch			no lunch			no lunch			no lunch			no lunch		
Kenneth Blanchard	500	330	10½	630	530	11	600	330	9½	530	500	11½	500	200	9

51.5

EQUIPMENT USED

	MATERIAL	DESCRIPTION OF WORK	EXPENSES
MONDAY	6/11/12	Tractor Trailer - Bld #121 Teter Bowing more cat Roller, milling machine P-6 to Bld #121 more JD Backhoe, sakai Roller NFS to Bld #121 more fence post 30 ft Electric gate Bld #121 to Ranes boat club - per mile	
		WEATHER: TEMP:	
TUESDAY	6/12/12	4218 Dump truck 10 loads of fill P-6 to South end Tractor Trailer - 310 Backhoe yard to Bld 121 - 310 Backhoe Bld 121 to yard repairs	
		WEATHER: TEMP:	
WEDNESDAY	6/13/12	Bld 121 Dump Truck 1 load from Bld. 121 to NFS Tractor Trailer 310 back fence P-6 to Bld 121 310 Backhoe Bld 121 to NFS 5510 power NFS to Bld 121 milling machine Bld 121 to P-6	
		WEATHER: TEMP:	
THURSDAY	6/14/12	Bld. 121 - Dump truck 4 loads of asphalt Quarry to Bld #121	
		WEATHER: TEMP:	
FRIDAY	6/15/12	Bld #121 Tractor Trailer cat Roller, sakai Roller Bld 121 to P-6 310 Backhoe Bld 121 to P-6 5510 power Bld 121 to NFS DD24 roller, 310 backhoe NFS to Back-club & Ranes per mile	

PMC

PAVING MATERIALS & CONSTRUCTION CO., INC

616 WEST FIRST AVENUE, ROSELLE, NJ 07203

TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 421B

PMC SUPERVISOR:

WEATHER: SUNNY

DATE: 6-15-12 (Friday)

TEMPERATURE: 71° AM 81° PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	[illegible]
1	A. LaGarella	O	H	8
2	D. Cordero	L	B	8
3	V. Duarte	L	B	8
4	S. Guardado	L	B	8
5	Green Willie	L	B	8
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 40

DESCRIPTION OF WORK:

DESCRIPTION OF WORK: LOCATIONS/STATIONS/ITEMS

Clean up Mill Area work on Full Box Area

Set up 3 Manholes to finish grade

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
[illegible]	50 Backhoe	[illegible]			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
43.39	TONS	DGA	Farmrad

SUBCONTRACTORS:

NAME	WORK PERFORMED
[illegible]	Millings
Polaris	3 Loads of Black to to welsen
[illegible]	2 loads of DGA

PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny

DATE: 6-14-12 (Thursday)

TEMPERATURE: 66° AM 79° PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. Matias	F		8.5
2	A. Madrigal	O	H	8.
3	D. Cordaso	L	B	8
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 24.5

DESCRIPTION OF WORK:

DESCRIPTION OF WORK LOCATIONS/STATIONS/ITEM
Mill Area to provide 2" to finish grade

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 70	Miller				

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY	DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED
Roy	
PK	Milling to norfolk
Polaris	

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Cloudy & Drizzel

DATE: 6-13-12 (Wednesday)

TEMPERATURE: 58° AM 77° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	BEGIN TOTAL
1	A. LaCanella	O	A	8.5
2	D. Grosso	L	B	8
3	J. Guardado	L	B	2
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 18.5

DESCRIPTION OF WORK:

DESCRIPTION OF WORK (LOCATIONS/STATIONS/ITEMS)
SUB GRADE AND D.G.A

P.M.C. EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIAL	SUPPLIER
484.48	TONS	DGA	Tennant

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC

PAVING MATERIALS & CONSTRUCTION CO., INC

616 WEST FIRST AVENUE, ROSELLE, NJ 07203

TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Cloudy

DATE: 6-12-12 (Tuesday)

TEMPERATURE: 62° AM 76° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. LAGANELLA	O	A	8
2	D. CORDASO	L	B	8
3	J. GUARDADO	L	B	8
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 24

DESCRIPTION OF WORK:

DESCRIPTION OF WORK: LOCATIONS / STATIONS / ITEM
WORK ON SUB BASE AND DGA.

PMC EQUIPMENT:

EQUIP #	EQUIPMENT TYPE	HOURS	EQUIP #	EQUIPMENT TYPE	HOURS
# 79	50 BACKHOE	4			
# 41	CAT DOZER	2			
# 18	HV PAC ROLLER	2			

RENTAL EQUIPMENT:

EQUIP #	EQUIPMENT TYPE	HOURS	EQUIP #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 421B

PMC SUPERVISOR: MCL

WEATHER: over cast w/ Sunny

DATE: 6-11-12 (Monday)

TEMPERATURE: 61° AM 75° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	RATE	TOTAL
1	A. LaGrenella	O	B	8
2	D. Cordoso	L	B	8
3	S. Guardado	L	B	8
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 24

DESCRIPTION OF WORK:

DESCRIPTION OF WORK & LOCATIONS / STATIONS / ITEM
Work on Sub Grade and D.GA

RMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 28	JD Backhoe	6			
# 18	Hypac	2			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	TYPE OF WORK PERFORMED

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, N.J. 07203

FOREMAN:

WEEK ENDING 6/9/12

DATE	6/4/12			6/5/12			6/6/12			6/7/12			6/8/12		
DAY	MONDAY			TUESDAY			WEDNESDAY			THURSDAY			FRIDAY		
JOB NO	4227			4227			4218			4218/4227			4227		
DESCRIPTION	Dump Truck			Dump Truck			Dump Truck Trash Truck			Dump Truck			Dump Truck		
EMPLOYEE										No Cert					
Kenneth Blauvelt			8	530	230	8½			8	630	330	9			8

41½

=

X

EQUIPMENT USED

	MATERIAL	DESCRIPTION OF WORK	EXPENSES
MONDAY	6/4/12	4227 - Dump Truck 1 - load of 3/4 stone Quarry to NFS 4 - loads of ~~DgA~~ RCA Quarry to NFS WEATHER: TEMP:	
TUESDAY	6/5/12	4227 - Dump Truck 2 loads of ~~DgA~~ RCA Quarry to NFS 1 load of 3/4 stone Quarry to NFS more loads of RCA from pile to pipe Trench WEATHER: TEMP:	
WEDNESDAY	6/6/12	4218 - Dump truck 1 load of broken asphalt P-6 to Quarry 1 load of DgA Quarry to P-6 Tractor Trailer more storage contain P-6 to NFS WEATHER: TEMP:	
THURSDAY	6/7/12	4218 - Dump truck - more 2 loads of fill 4217 - Dump Truck - more loads of fill 40 load WEATHER: TEMP:	
FRIDAY	6/8/12	~~4218~~ - Dump Truck 4227 more loads of fill 35 load	

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny

DATE: 6-8-12 (Friday)

TEMPERATURE: 61° AM 77° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	RATE	TOTAL
1	A. Matias Star 6:30	F	B	8.5
2	A. Madrigal	O	A	8
3	A. Laganella Star 6:30	O	A	8.5
4	D. Cardoso	L	B	8
5	J. Guardado	L	B	8
6	J. Rocha	L	B	8
7	V. Duarte	L	B	8
8	Grevir Willie	L	B	8
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 65.00

DESCRIPTION OF WORK:

DESCRIPTION OF WORK: LOCATIONS/STATIONS/ITEM #

Work on Toll Sub Grade And D.G.A. Area Remove water barrier from P6 into yard. Go to Heterboro Drop off Drums to close Area for Monday Set up Lane close for Dumor on Brewster Rd.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 29	JD Backhoe	4			
	CAT Dozer D5	4.5			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC

PAVING MATERIALS & CONSTRUCTION CO., INC.

616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4219 | Yard

PMC SUPERVISOR: Mel

WEATHER: Sunny

DATE: 6-7-12 (Thursday)

TEMPERATURE: 63° AM 77° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	BEGIN TOTAL
1	A. MATIAS (YARD 8)	F		8
2	A. MADRIGAL	O	A	8
3	A. LA CANNELLA Start: 6:30 AM	O	A	8.5
4	D. CARDOSO	L	B	8
5	J. ROCHA	L	B	8
6	J. GUARDADO	L	B	8
7	V. DUARTE (YARD 8)	L	B	~~8~~
8	GUION JR WILLIE (YARD 8)	L	B	~~8~~
9				
10				
11				
12				
13				
14				

(24)

TOTAL HOURS WORKED: 40½

DESCRIPTION OF WORK:

DESCRIPTION OF WORK	LOCATIONS / STATIONS / ITEM
WORK AREA BY TOLL BOTH SUB GRADE AND DGA	
WORK ON YARD FIX BARE AREA OF TOP SOIL SEED.	
FINISH PAINT AND MULCH	

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
H 28	J.D. Backhoe	4			
H	Cat Dozer	4.5			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
382.76	tons	x D G. A	Danwood

SUBCONTRACTORS:

NAME	WORK PERFORMED

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218 / Yard

PMC SUPERVISOR: Mel

WEATHER: Sunny

DATE: 6-6-12 (Wednesday)

TEMPERATURE: 61° AM 78° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME		CLASSIFICATION CLASS	RATE	TOTAL
1	A Matias	YARD 8h	F		
2	A. Madrigal		O	A	8
3	A Laganella		O	A	8
4	D. Cordoso		L	B	8
5	J. Guardado		L	B	8
6	Greenjr. Willie	YARD 8h	L	B	~~8~~
7	V. Duarte	YARD 8h	L	B	~~8~~
8	J. Rocha		L	B	8
9			L	B	8
10					
11					
12					
13					
14					

(24)

TOTAL HOURS WORKED: 40

DESCRIPTION OF WORK:

DESCRIPTION OF WORK & LOCATIONS / STATIONS / ITEM

Dig out trench for Pantelleo move storage box from P6 into Norfolk. Antonio did oil change on cat roller

Work on yard remove tree out of the back paint entrance door change lights outside

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
4-28	T.D. BACKHOE	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: cloudy & sunny

DATE: 6-5-12 (Tuesday)

TEMPERATURE: 53° AM 73° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL HOURS
1	A. MATIAS	F		8
2	A MADRIGAL	O	A	8
3	A LAGANELLA	O	A	8
4	D. CORDOSO	L	B	8
5	J. GUARDADO	L	B	8
6	GREENTR WILLIE	L	B	8
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 48

DESCRIPTION OF WORK:

DESCRIPTION OF WORK * LOCATIONS / STATIONS / ITEM #
MARK OUT BEACH FOR PARTELLO AND SAW CUT.
GRADE BETWEEN CURB AND SIDE WALK FOR TOP SOIL
INSTALLING PAPER WRAP AROUND BUILDING MOVE TRAIL OFFICES
TO NEW LOCATION

P.M.C. EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 28	JD Backhoe	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC

PAVING MATERIALS & CONSTRUCTION CO., INC.

616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Nel

WEATHER: Rain

DATE: 6-4-12 (Monday)

TEMPERATURE: 55° AM 61° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:00 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	BEAT TOTAL
1	A. Matias 4h. (4218 / 4h. Yard)	F		8
2	A. Madrigal	O	A	8
3	A. Lagannella	O	A	8
4	D. Cordoso (Use bold time)	L	B	4
5	J. Guardado	L	B	2
6	Greenor Willie	L	B	2
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 32

DESCRIPTION OF WORK:

DESCRIPTION OF WORK: LOCATIONS / STATIONS / ITEM

Clean up area piles of asphalt + dirty. And grade area long side of Brewster Rd Antonio work on Hamtsu loader fix hydraulic hoses. And help me fix entrance gate at yard myself work yard spread mulch on shrubs.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 28	TD Backhoe	8			
# 32	TD excavator	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIAL	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PVC
PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot PG

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny

DATE: 6-1-12 (Friday)

TEMPERATURE: 62° AM 79° PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 3:00 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. Matias	F		8.5
2	A. Madrigal	O	A	8
3	T. Laganella	O	A	8
4	D. Cordoso	L	B	8
5	J. Guardado	L	B	8
6	Green Jr Willee	L	B	8
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 64.5
48%

DESCRIPTION OF WORK:

DESCRIPTION OF WORK: LOCATIONS / STATIONS / ITEM

Finish load concrete. Then load asphalt to weldon
Pour concrete for signs work on island grade them to 4" from
top curb to top soil

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 32	JD Excavator	8			
# 28	JD Backhoe	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY	DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED
Ray	Lay concrete and black top.

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, N.J. 07203

FOREMAN:

WEEK ENDING 6/30/12

DATE	6/25/12			6/26/12			6/27/12			6/28/12			6/29/12		
DAY	MONDAY			TUESDAY			WEDNESDAY			THURSDAY			FRIDAY		
JOB NO	4227			4227			4218/4227			4227			4227/ Tom		
DESCRIPTION	Dump Truck			Dump Truck & Tractor Trailer			Dump Truck			Dump Truck			Tractor Trailer		
EMPLOYEE	Volunteer			Volunteer			Volunteer			Volunteer			Volunteer		
Kenneth Blanchard	530	330	10	530	200	8½	530	300	9½	530	300	9½	500	300	10
47.5															

EQUIPMENT USED

	MATERIAL	DESCRIPTION OF WORK	EXPENSES
MONDAY	6/25/12	4227 - Dump truck 1-load of RCA Quarry to NFS NFS - water RCA and Roll RCA with 110 Roller WEATHER: TEMP:	
TUESDAY	6/26/12	4227 - Dump truck 1-load of ~~RCA~~ 3/4 stone Quarry to NFS Roll RCA with 110 Roller Tracks Trailer 310 dock yard to NFS 310 Roller & D024 Roller from Boat yard to NFS WEATHER: TEMP:	
WEDNESDAY	6/27/12	4218 - Dump Truck 1-load of asphalt Quarry to P-C 4227 - Dump Truck 1-load of 3/4 stone Quarry to NFS move 4 loads of fill at NFS Run 230 Trackhoe load trucks with fill WEATHER: TEMP:	
THURSDAY	6/28/12	4227 - Dump truck 1-load of RCA Quarry to NFS move & load load of fill at NFS with C44 loader put stone in truck, fill rest of the way with RCA go with Mike W to Bernardsville WEATHER: TEMP:	
FRIDAY	6/29/12	4227 - Tracks Trailer move 270 Trackhoe PC - to NFS Tom Bock - move 330 cat trackhoe NFS to Bernardsville	

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

WATER + ICE 32.00

DAILY JOB REPORT

JOB NAME: Lot PG

PMC JOB #: 4219

PMC SUPERVISOR: Mel

WEATHER: SUNNY

DATE: 6-29-30 (Friday)

TEMPERATURE: 78° AM 98° PM

CREW STARTS: 6:00 AM / PM

CREW FINISH: 3:00 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. MATIAS	F		5.5
2	A. MADRIGAL	O	A	8.5
3	D. CORDOSO	L	B	8.5
4	U. DUARTE	L	B	8.5
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: ~~24~~ 31

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS / STATIONS / ITEM	
Finish Hammer Black top on 5 signs and dig them out 2x2x2 Remove water barrier out to give back parking area.	
Myself work on teterboro	From 8:AM to 11:AM

PMC EQUIPMENT:

EQUIP #	EQUIPMENT TYPE	HOURS	EQUIP #	EQUIPMENT TYPE	HOURS

RENTAL EQUIPMENT:

EQUIP #	EQUIPMENT TYPE	HOURS	EQUIP #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot 96

PMC JOB #: 4218

PMC SUPERVISOR: Hel

WEATHER: SUNNY

DATE: 6-29-12 (THURS.)

TEMPERATURE: 78° AM 89° (PM)

CREW STARTS: 6:30 (AM) / PM

CREW FINISH: 3:00 AM / (PM)

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	Total
1	A. MATIAS	F		8.5
2	A. MARIGAL	O	A	8
3	D. CORDOSO	L	B	8
4	V. DUARTE	L	B	8
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 32.5

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS/STATIONS/ITEMS/QUANTITIES
DIG UP HOLES FOR SIGNS total (4) AND SAW CUT HOLE
The Remain STOP SIGNS on Lot to GIVE Back. total of (5)

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
#20	20 Backhoe	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIAL	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot C6

PMC JOB #: 4218

PMC SUPERVISOR: Hel

WEATHER: SUNNY

DATE: 6-27-12 (Wend)

TEMPERATURE: 65° AM 79 PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. Matias	F		8.5
2	A. Madrigal	O	A	8
3	A. Laganella	O	A	8
4	D. Cordoso	L	B	8
5	V. Duarte	L	B	8
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 40.5

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS / STATIONS / ITEM

Pave Area Small Patch. And Star Dig foundation for signs (4)
Dig trench for Pantheo electric. Antonio Wirte on Blaw Knox
Paver Serviced on oil fuel filter. #48

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
248	Backhoe	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIAL	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Rehab Parking Lot P-6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny

Wed
DATE: 6-27-12

TEMPERATURE: 70° AM 75° PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 9:00 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME		CLASSIFICATION CLASS	RATE	Total
1	B. LaSala		F	B	3
2	~~T. Laganella~~				
3	R. Drude DRUDE		O	A	2½
4	G Tomas		F	B	2½
5	J. Guardado		L	B	2½
6	W. Green		L	B	2½
7	J. DaRocha	on Rave Card	L	B	~~2½~~
8	V. Duarte	on Auger Card	L	B	~~2½~~
9					
10	T Laganella	on Auger Card	O	A	~~2½~~
11	D. Cardoso	on Auger Card	L	B	~~2½~~
12					
13					
14					

TOTAL HOURS WORKED: 13

DESCRIPTION OF WORK:

DESCRIPTION OF WORK: LOCATIONS / STATIONS / ITEM

Pave 2 passi to correct water problem

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
68	Tool Truck	8			
"	~~[illegible]~~	8			
87	Cat Paver	8			
69	Cat Roller	8			
20	Sabai Roller	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
73.05 X	Tons	W MAPA T-5 W/6	Weldon (W)

SUBCONTRACTORS:

NAME	WORK PERFORMED
AnS Consultants	

PMC

PAVING MATERIALS & CONSTRUCTION CO., INC

616 WEST FIRST AVENUE, ROSELLE, NJ 07203

TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny & Breeze

DATE: 6-26-12 (Tuesday)

TEMPERATURE: 63° AM 77° PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. Matias	F		8
2	A. Madrigal	O	A	8
3	A. Laganella	O	A	8
4	D. Cordoso	h	B	8
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 33

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS / STATIONS / ITEM #

Mill Area 2" Depht. Saw Cut Key Ways And Swepht.
Install Concrete Surround For Signs Post. Antonio Mill and work
on Blow-Know Paver #48 Stay to Close Gate For R.C.C.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
#28	[illegible]	9			
#70	Miller 2000	2			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIAL	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4219

PMC SUPERVISOR: Neel

DATE: 6-25-12 (Monday)

CREW STARTS: 6:30 AM / PM

WEATHER: Overcast Rain on and off

TEMPERATURE: 63° AM 76° PM

CREW FINISH: 3:00 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. Matias 6:00 AM	F		8.5
2	A. Madrigal 6:00 AM	O	A	8.5
3	A. LaGanella	O	A	8
4	D. Cordoso	L	B	8
5	Green JR Willie	L	B	8
6	V. Duarte (OFF)	—	—	—
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 41

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS, STATIONS, ITEMS

Back fill pipe trench (Verizon) Clear Phase 3 Area Remove Broken concrete and move storm. Drain pipe out of way Antonio worked on JD excavator Do oil change and set roller

PMC EQUIPMENT:

EQUIP #	EQUIPMENT TYPE	HOURS	EQUIP #	EQUIPMENT TYPE	HOURS

RENTAL EQUIPMENT:

EQUIP #	EQUIPMENT TYPE	HOURS	EQUIP #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIAL	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, N.J. 07203

FOREMAN:

WEEK ENDING 6/23/12

DATE	6/18/12			6/19/12			6/20/12			6/21/12			6/22/12		
DAY	MONDAY			TUESDAY			WEDNESDAY			THURSDAY			FRIDAY		
JOB NO	4218/4227			4218/4227			4227			4227			4227		
DESCRIPTION	Dump Truck			Dump Truck			Dump Truck & Tractor Trailer			Dump Truck & 644 loader			Dump Truck		
EMPLOYEE	no lunch			no lunch			no lunch			no lunch			no lunch		
Kenneth Blanchard	500	330	10½	500	330	10½	500	330	10½	630	330	9	530	230	9
49.5															

EQUIPMENT USED

	MATERIAL	DESCRIPTION OF WORK	EXPENSES
MONDAY	6/18/12	4218- Dump truck 1 load of plant mix Quary to P-6 4227- Dump truck move RCA from pile and dump into paver NFS WEATHER: TEMP:	
TUESDAY	6/19/12	4218- Dump truck 1 load of plant mix Quary to P-6 4227- Dump truck 4 loads of RCA from Quary to NFS move RCA from pile and dump into paver at NFS, load truck with 644 4 loads WEATHER: TEMP:	
WEDNESDAY	6/20/12	4227- Dump truck 4 loads of RCA from Quary to NFS #8 dump truck - tube blew apart on truck stuck on Rt 78, wait for auto and get tractor truck load and bring truck to yard WEATHER: TEMP:	
THURSDAY	6/21/12	4227- use 644 loader, load dump truck with fill - all day go to yard help auto finish truck bring back to NFS, dump load of stone WEATHER: TEMP:	
FRIDAY	6/22/12	4227- Dump truck 2 loads of RCA Quary to NFS Reen water Truck - at NFS water stone	

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot P6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: SUNNY

DATE: 6-22-12 Friday

TEMPERATURE: 73° AM 89° PM

CREW STARTS: 6:00 AM / PM

CREW FINISH: 3:00 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	RATE	TOTAL
1	A. MATIAS	F		8.5
2	A. MADRIGAL	O	A	8
3	A. LAGANILLA	O	A	8
4	D. CORDOSO	L	B	8
5	V. DUARTE	L	B	8
6	GREEN JR WILLIE	L	B	8
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 48.5

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS / STATIONS / ITEM

TAKE DOWN WRAP PAPER AT BUILDING AND PUT UP NEW one LOAD DIRT to SOUTH and NEW LOCATION USE A TRUCK ANTONIO WORK on shop PUT ND BACKHOE BACK TO GETHER NEW PARTS.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
#42	50 excavator	[illegible]			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER

SUBCONTRACTORS:

NAME	WORK PERFORMED
PK	take out FILL off PG to south end
Scinto	2 loads of Broken Asphalt to welcome

Expenses 25.00
74.97

PMC

PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Rehab Parking Lot P-6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny - Hot - Humid

DATE: Thurs 6-21-12

TEMPERATURE: 85° AM 100 PM

CREW STARTS: 5:30 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	B LaSala	F	B	11
2	~~R. Sopre~~ See his time card	~~F~~	~~A~~	~~11~~
3	G Tomas	F	B	11
4	T Lagamilla	O	A	12
5	R. Drude	O	A	12
6				
7	J. Nieto	L	B	11
8	J Da Rocha	L	B	11
9	J Guandado	L	B	11
10	D. Condoso	L	B	11
11	V. Duarte	L	B	11
12	W Green	L	B	11
13				
14				~~11~~

TOTAL HOURS WORKED: 113

DESCRIPTION OF WORK:

DESCRIPTION OF WORK / LOCATIONS / STATIONS / ITEMS
Laurel Lot - Finish Pave Parking Lot

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
68	Tool Truck	8			
82	CAT Paver	8			
69	CAT Roller	8			
20	Sakai Roller	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
884.86	Ton	X WMA PA I-5A W/6	Walton (W)

SUBCONTRACTORS:

NAME	WORK PERFORMED
A-S Consultants	

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

6.00 EXPENSES

DAILY JOB REPORT

JOB NAME: NFS

PMC JOB #: 4227 / 4218

PMC SUPERVISOR: Mike W.

WEATHER:

DATE: 6-21-12 (Thursday)

TEMPERATURE: _____ AM _____ PM

CREW STARTS: _____ AM / PM

CREW FINISH: _____ AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	Angie Matias	F		9
2	Antonio Madrigal	O		9
3	Ryan Whitehead	L	B	9
4				
5	Rance Soper (4218)	F/O		10
6				
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 27 / 10

DESCRIPTION OF WORK:

DESCRIPTION OF WORK / LOCATION / STATION / ITEM
Dumping stone in piles and grading off with dozer.
Excavation and moving material to East end and grading off. Loaded and moved (20 loads)
Tran paver at P-6 for Billy
20 Loads
Polaris - 2 loads RCA from Plant
20 - loads on site excavation

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
	750 dozer	8			
	Cat 330 trackhoe	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
1881.94	tons	X RCA Stone 75 loads	Denwood

SUBCONTRACTORS:

NAME	WORK PERFORMED
1- Polaris truck 8 hrs.	

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Rehab Parking lot R-6

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: Sunny

DATE: Wed 6-20-12

TEMPERATURE: 95 AM 100 PM

CREW STARTS: 6:30 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION: CLASS	CLASSIFICATION: RATE	TOTAL
1	B LaSala	F	B	11
2	G Tomas	F	B	10
3	T Laganella	O	A	9½
4	R. Brude	O	A	10
5				
6	J Guardado	L	B	9½
7	J Da Rocha	L	B	9½
8	W. Green	L	B	9½
9	D. Cardoso	L	B	9½
10	V. Duarte	L	B	9½
11		L	B	9½
12		L	B	
13		L		
14				

TOTAL HOURS WORKED: 88

DESCRIPTION OF WORK:

DESCRIPTION OF WORK / LOCATION / STATION / ITEM

Level Parking lot.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
68	Tool Truck	8			
87	CAT Paver	8			
69	CAT Roller	8			
20	Sakai Roller	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
565.27	Tons	X WMA PAI-5A W/6	Waldon (W)
117.26	Ton	X NJ DOT D6A / Type 5A	Waldon (W)

SUBCONTRACTORS:

NAME	WORK PERFORMED
A-S Consultants	
Apgar Sweeping	
Falcon	

PMC
PAVING MATERIALS & CONSTRUCTION CO., INC
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

DAILY JOB REPORT

JOB NAME: Lot 86

PMC JOB #: 4218

PMC SUPERVISOR: Mel

WEATHER: SUNNY

DATE: 6-19-12 tuesday

TEMPERATURE: 73° AM 81° (PM)

CREW STARTS: 6:30 (AM) / PM

CREW FINISH: 3:00 AM / (PM)

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	RATE	TOTAL
1	A. Matias	F		8
2	A. Madrigal	O	A	8
3	A. Lagamella	O	A	8
4	D. Cordero	L	B	8
5	V. Duarte	L	B	8
6	Green Jr Willie	L	B	8
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 48

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS / STATIONS / ITEM #
Fill Box Area with hot Rock and finish clean up
Key way. Antonio work on equipment do oil change.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
[illegible]	D Backhoe	[illegible]			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
25.04	tons	Shot Rock	

SUBCONTRACTORS:

NAME	WORK PERFORMED

PAVING MATERIALS & CONSTRUCTION CO., INC.
616 WEST FIRST AVENUE, ROSELLE, NJ 07203
TEL: 908-241-2424 FAX: 908-241-2420

Expenses
Ice + Water 40.00

JOB NAME: Lot P6

PD w/E 6/30/12

DAILY JOB REPORT

PMC JOB #: 4219

PMC SUPERVISOR: Neil

WEATHER: Sunny

DATE: 6-18-12 Monday

TEMPERATURE: 58° AM 77° PM

CREW STARTS: 7:00 AM / PM

CREW FINISH: 3:30 AM / PM

EMPLOYEES:

	EMPLOYEE'S NAME	CLASSIFICATION CLASS	CLASSIFICATION RATE	TOTAL
1	A. Matias	F		8
2	A. Madrigal	O	A	8
3	A. LaGanella	O	A	8
4	V. Duarte	L	B	8
5	D. Cardoso	L	B	8
6	Gree Jr Willie	L	B	8
7				
8				
9				
10				
11				
12				
13				
14				

TOTAL HOURS WORKED: 48

DESCRIPTION OF WORK:

DESCRIPTION OF WORK - LOCATIONS / STATIONS / ITEM #

Fill up trench with hot Rock Back Fill Pipe trench Dirt
And D.G.A. Prep Hole Areas for hot Rock.

Antonio work on JD Backhoe Pull out Radiator to be Prepare
And stop at P6 to mill hight spots And went to Norfolk
to fix hose on JD Dozer.

PMC EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS
# 29	5D Backhoe	8			

RENTAL EQUIPMENT:

EQUIP. #	EQUIPMENT TYPE	HOURS	EQUIP. #	EQUIPMENT TYPE	HOURS

MATERIALS:

QUANTITY		DESCRIPTION OF MATERIALS	SUPPLIER
25.09	tons	X hot Rock	Weldon

SUBCONTRACTORS:

NAME	WORK PERFORMED

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. /

Weather: (A.M.) Sunny : 63° /(PM) Sunny : 76°

Activity (PMC) Continued and completed the grading work - west of proposed entry / exit canopy plaza

CLASSIFIED ITEM No 11. PLANT MIX MACADAM, PER TON.
Contractor performed pavement / trench restoration using plant mix @ area located west of proposed plaza.
- Total of 25.00 Tons of plant mix been used today.

Manpower:
1- Supervisor
1- Operator
1- L/F
3 - Laborer

EQP'T.
2 Combination hoe 310 SE / 310 JD
1- Plate tamper
1- P/U Trk. F-350

Pavement and trench restoration on going.
Existing pavement surface preparation for paving also on going.
Pantaleo crew (Surface and underground crew on site)
- Safety officer Eve Murphy visited the site. No safety issue.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-18-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/18/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		X
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		X
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		X
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		
OXENREIDER	MELVIN	PMC	**10/8/2012**		
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		X
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		
MEYER	STEPHEN	LET IT GROW	5/10/2015		
SOTO	TONY	LET IT GROW	5/14/2015		
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		
MARCO	MIRASSOL	LET IT GROW	2/8/2015		
LOPEZ	MARCO	LET IT GROW	TEMP		
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION INC. R.S. ~~Pantaleo Electric, Inc.~~ **Contract Number:** EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Monday June 18, 2012

Weather - AM Temp N/A PM - N/A degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician 1 Operator 2 laborers

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Pantaleo ground crew workers are excavating, leveling and handholes for new pole lightingduct banks on northeast side of P6 Ground crew workers backfilled around each Hand hole they set clearing a path along the barrier wall in preporation for the ductbank. Workers had to reverify the proper elevations and distance prior to each HH placement. Workers continued pulling in conductors from the polr bases to each previously set Hanhole.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-~~N/A~~

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Monday 18 June 2012

Signed RONALD STRIBUTO **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/18/12 Monday WEATHER Sunny TEMP: AM 60 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC worked on trench restoration with plant mix in stage I west in am
					Clean/prep/grade area for paving
					Pantaleo start installing HH's in Stage IIID. Work on UG conduit in canopy islands. Still waiting on island
					boxes for canopy islands.
DUMOR					Wiring light poles in stage I west
Super					
OE					
Laborer					Notified by Mel O. of PMC that Railroad Construction will return Thursday to work on misc steel for
PMC	super	1			canopy.
	OE	1			
	LF	1			
	laborer	3	1		
	trucks				
LET IT GROW					
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
Pantaleo		6			
ANS	technicians				
APGAR	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		12	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 2

Weather: (A.M.) Sunny: 55° /(PM) Sunny: 77°

ACTIVITY (PMC) Performed clean up and surface preparation for paving @ area west of proposed entry / exit plaza
- Loaded out materials that have been removed
- Surface preparation for paving on going.
- Performed saw cutting of existing asphalt pavement

Manpower:	EQP'T.
1- Supervisor	1- B/H JD combination hoe 310 SJ
1- Operator	1- Box truck
4- Laborer	1- F-350 P/U Trk.

ACTIVITY 2: LET IT GROW (SUB) continued the landscaping work - north of Stage 2, and @ area south of entry / exit plaza.
Planting of shrubs also continued.
- Also continued the placement of stabilized crushed screenings into joints of splash pavers.

Note: I notified Angel Berrios, Parking lot Supervisor, about Let It grow crew that coming in tomorrow @ P6 (Saturday, June 16, '12, to water the plants, and shrubs that have been planted.

Manpower:	EQP'T
1- Supervisor; 1-L/F; 2- Operator; 5- Laborer	1- Irrigation trk, 1- skid steer; 2- Van
PANTALEO on SITE - only surface crew (2-MP)	1- Mini 4 hoe; 1- Bob Cat T300; Utl. P/U Trk.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 pm

Date 6-15-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE

PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 2 / 2

Weather: (A.M.) Sunny / (PM) Sunny

ACTIVITY 1: CLASSIFIED (WORK) ITEM No. 10. BASE COURSE, PER SQ. YD.
Contractor delivered DGABC today for base.
Total of 21.09 C.Y. have been delivered today.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-15-12

Signed [illegible] **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/15/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		X
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		X
OXENREIDER	MELVIN	PMC	**10/8/2012**		
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		X
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		X
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
LOPEZ	MARCO	LET IT GROW	TEMP		X
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE

Contractor: PAVING MATERIAL AND CONSTRUCTION CO. INC. ~~Pantaleo Electric, Inc.~~ R.S.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Friday June 15, 2012

Weather - Partly cloudy - AM 69 degrees - PM - Partly Cloudy 79 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Pantaleo workers excavated and trenched out conduits running inside of the toll booth islands in preperation of conduit encasement.

Workers made final adjustments toconduit stub ups and offsets extending the underground conduits previous placed up to final grade..

Workers dropped conductors down from top of poles to bases .

Workers placed concrete around conduits in island under canopy in designated spots to encase conduits.

Workers placed concrete around the conduits entering the relocated Handhole at the service building.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-~~N/A~~ POURED APPROX. 6 YDS OF CONCRETE TO COVER CONDUITS AND FORM DUCTBANK

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Friday 15 June 2012

Signed RONALD STRIBLING

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 (07-11)

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 1

Weather: (A.M.) CLOUDY :57° /(PM) Partly Sunny : 75°

ACTIVITY 1: CLASSIFIED (WORK) ITEM Nº 1. MILL ASPHALT CONCRETE TO 2" BELOW FINISHED GRADE, PER SQUARE YARD.

- PMC resumed milling work - west of proposed entry/exit plaza.
- Milling @ west section completed.
- Total of 1,657.61 have been milled today (see attached sketch)

Manpower:	EQP'T
1- Supervisor	1- Milling Machine Wirtgen W 2200
1- Operator	2- D/Tnk.
1- L/F	1- F-650

ACTIVITY 2: LET IT GROW (SUB) Continued landscaping work @ stage 2 North, and on island located east of existing lift station.

- Planting shrubs on going.

Architect James Loudon, visited the site. checked landscaping work - All acceptable.

Manpower:	EQP'T	
1- Supervisor	1- JD Mini 4 hoe	2 - F 50 VAN
2- Operator	1- Bob cat T 300 skid steer	1- Irrigation Van 350
6- Laborer	1- P/L 580 M	2- UTL. P/U Tnk

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-14-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

Work Sheets	1 OF 1	**Charito L. Hernandez**
REHABILITATION OF PARKING LOT P6 **EWR- 154.028**		**Date:** 6-14-12
		Weather: (A.M.) C-57° /(P.M.) S-75

STAGE 1

Activity:

Classified Item No.1: MILL ASPHALT CONCRETE TO 2" BELOW FINISHED GRADE, PER SQUARE YARD

Computations:

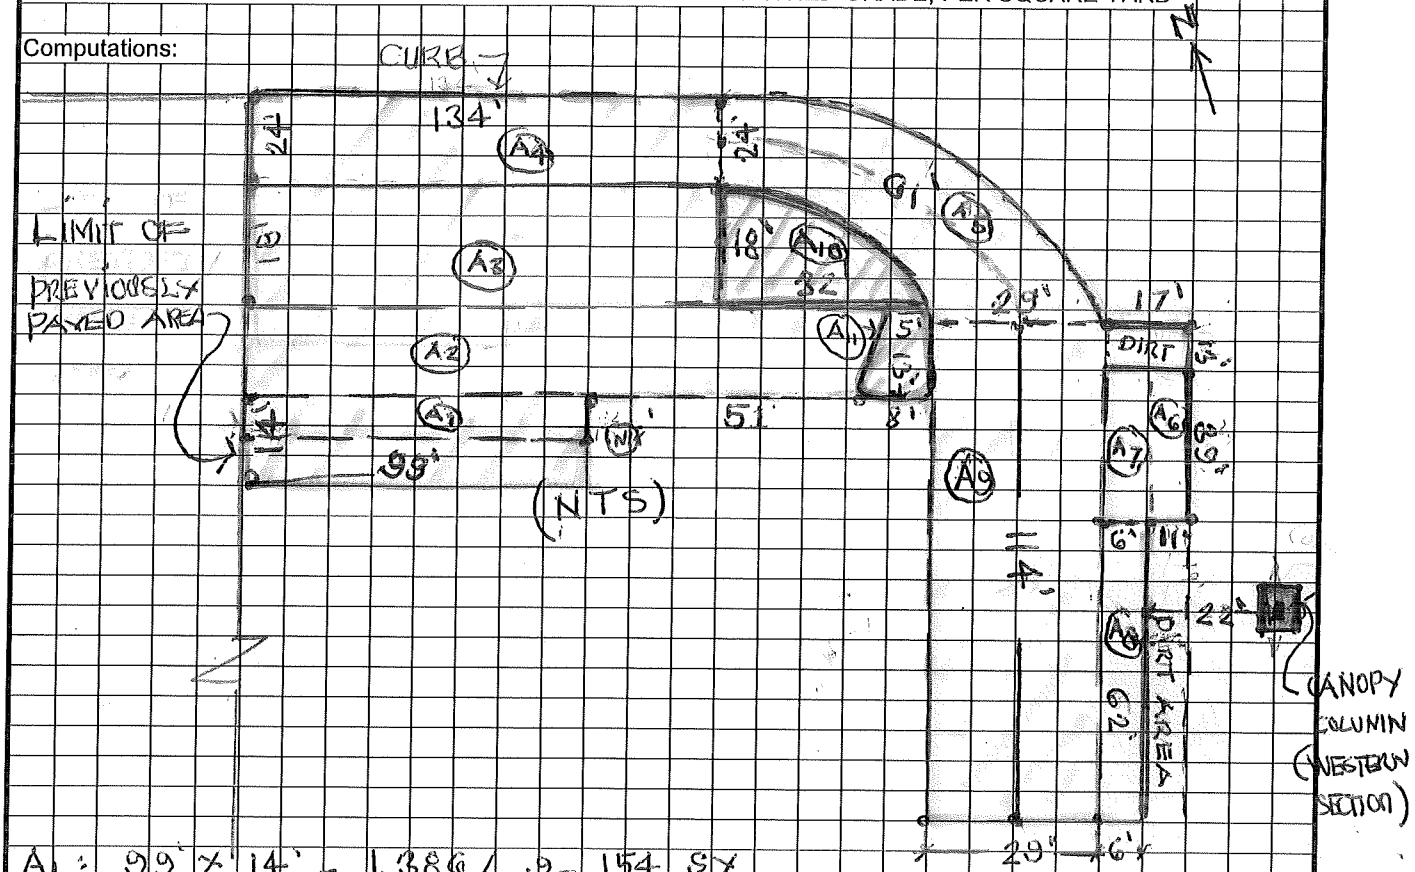

A1: 99' x 14' = 1,386 / 9 = 154 SY

A2: 150' x 13' = 1,950 / 9 = 216.67 SY

A3: 134' x 18' = 2,412 / 9 = 268 SY

A4: 134 x 24' = 3,216 / 9 = 357.33 SY

A5: $\left(\frac{29+24}{2}\right)$ 61 x 26.5 = 166.5 / 9 = 179.61 SY

A6: 39' x 11' = 429 / 9 = 47.67 SY

A7: 39' x 6' = 234 / 9 = 26 SY

A8: 62' x 6' = 372 / 9 = 41.33 SY

A9: 114 x 29' = 3306 / 9 = 367 SY

Area of Island:

A10: (.5) 18' x 32 = 288 / 9 = 32 SY

A11: $\left(\frac{8+5}{2}\right)$ 13' x 6.5 = 84.5 / 9 = 9.39 SY

Area of Island: 32 + 9.39 = 41.39 SY

TOTAL AREA MILLED:

A1 to A9

= 1,657.61 SY

LEGEND:

---- Area Milled

EWR 154.028 PARKING LOT P6		DATE	6/14/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		X
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		X
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		
GUARDADO	DOAQUIN	PMC	**PENDING**		
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		
LAGANELLA	TONY	PMC	8/10/2012		
MADRIGAL	ANTONIO	PMC	**5/12/2012**		X
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		X
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
LOPEZ	MARCO	LET IT GROW	TEMP		X
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: ~~Pantaleo Electric, Inc.~~ PAVING MATERIALS AND CONSTRUCTION CO. INC. **Contract Number:** EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Thursday June 14, 2012

Weather - Partly cloudy - AM 65 degrees - PM - Partly Cloudy 79 degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- PANTALEO ELECTRIC INC.

Pantaleo Ground crew workers excavated and trenched out for the remaining handholes and pole bases for P6 Northwest side.

Workers continued the excavation and trenching for the lighting ductbank s and set (2) pole bases and set handhole structures.

Workers pulled in pole lighting circuits from the pole bases to the handhole's. Workers dropped conductors down poles to bases.

Workers drilled out curbs for conduit sleeve for loop detectors. (Vehilce detection sensors)

Workers drove ground rods under canopy at each column, and a couple around the north and west side of service bulding. The rods driven were drove with no direction or ground plan. No wire were connected to driven rods.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Thursday 14 June 2012

Signed RINALDO STRIBLINO **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/14/12 Thursday WEATHER Sunny TEMP: AM 65 PM 71

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC - mill stage I west, saw-cut west edge
					Let it grow continue planting of shrubbery. Install pavers at hot box. Jin Loudon site visit late am
					Pautaleo - relocate HH interfering with pedestrian walkway in ne corner of service building
DUMOR					Continue on ug conduit in island areas under canopy. Delivery of two LP fdn's and 3 HH in pm
Super					
OE					Mayflower arrived in early morning to spackle but left site after realizing roof is not complete on the
Laborer					Service Building
PMC	super	1			
	OE	1			Site visit by Eve Murphy in pm.
	LF	1			
	laborer	1			
	trucks	3			
LET IT GROW		9			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
Pantaleo		6			
ANS	technicians				
APGAR	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		22	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 p/u, 1 Dozer, 1 Bobcat dozer/backhoe

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 1

Weather: (A.M.) 61° - Drizzle /(PM) Cloudy + 75°

ACTIVITY: (PMG) Continued grading west of existing lift station
CLASSIFIED (WORK) ITEM No. 10 (BASE COURSE, PER CUBIC YARD.
Contractor continued the delivery and spreaded of DGABC for base course located west of existing lift station.
Total of 242.24 CY. have spreaded today.
Base preparation on going.

Manpower:	EQP'T
1-Supervisor	1-Dozer D5M LGP CAT
1- Operator	1- Roller C778B
1- Laborer	1- combination hoe 310 SS

ACTIVITY 2: LET IT GROW (SUB) Continued landscaping work - north and south of proposed canopy plaza (installation of salt splash pavers and tree planting
- All landscaping work on going.

Manpower:	EQP'T
1- Supervison	1- Concrete saw
1- L/F	2 - Van Service truck
4- Laborer	1- Skid steer

PANTALEO ground and surface crew on site today - 2 - Surface crew; 4 - underground crew)

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 9-13-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/13/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		X
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		X
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/13/12 Wednesday WEATHER Cldy/rain TEMP: AM 65 PM 71

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Let it grow continue paver installation on the southeast island from canopy (cut pieces)
					Continue on tree planting along Brewster Road (drive tree stakes, fertilize)
					Pantaleo continue on canopy island ug conduit. Return of UG crew for installing light pole foundations in Stage I , west of canopy 90E & 65D.
DUMOR					
Super					DGABC deliveries and placement in the west side of Stage I
OE					
Laborer					Delivered milling machine in afternoon
PMC	super	1			
	OE	1			Aon site visit in late am
	LF				
	laborer	1			Falcon surveyor on site in am
	trucks				
LET IT GROW		6			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor	1			
Pantaleo		6			
ANS	technicians				
APGAR	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		16	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 p/u, 1 Dozer, 1 Bobcat dozer/backhoe

PMC utilizing 310SJ BH & D5M dozer

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: ~~Pantaleo Electric, Inc.~~ PAVING MATERIAL AND CONSTRUCTION CO. INC. R.S.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Wed June 13, 2012

Weather - Partly cloudy - AM 65 degrees - PM - Partly Cloudy 79 degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- PANTALEO ELECTRIC INC.

Pantaleo Ground crew workers excavated and trenched out for the remaining handholes and pole bases for P6 Northwest side.

Workers continued the excavation and trenching for the lighting ductbank s and set (4) pole bases and set handhole structures.

Workers pulled in pole lighting circuits from the pole bases to the handhole's.

Workers relocated electrical Hanhole behind the service building to clear the handicap ramp. Conduits were rerouted and reconnected into the ductbank awaiting conduit enbcasement.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Wed 13 June 2012

Signed RONALD STREBLING

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

DAILY NARRATIVE

PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 2

Weather: (A.M.) Cloudy : 64° /(PM) 72° - Rainy

ACTIVITY 1: (NET COST) DWG- G005, GEN. NOTES 11L. TRANSPORTATION OF SOIL FROM SITE TO STOCKPILE AREA.

- Contractor resumed hauling out of excess unsuitable material from P6, to stockpile yard @ south end of EWR (inside Gate 1.
- Hauling out on going.

Manpower:	EQP'T
1- Operator	1- Combination hoe JD 310 SJ
1- Driver	1- Dump Truck

PMC- Continued rough grading (west of existing lift station) @ stage 1.

- Performed proof rolling of existing sub-base.
- Continued misc. clean up.
- All work on going.

Manpower:	EQP'T.
1- Operator	1- Combination hoe JD 310 SJ
2- Laborer	1- Roller CB 778B

LET IT GROW (SUB) Continued landscaping work- south of proposed canopy plaza. Also continued tree planting activity, north of Stage 1.

- All work on going.

Manpower (see next sht).

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM – 3:30 PM

Date 6-12-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 2 / 2

Weather: (A.M.) Cloudy : 64° /(PM) 72° - Rainy

Manpower (Let it Grow)

1- Supervisor
1- L/E
3-Laborer

EQPT.

1- Concrete saw
2- Van F-150
1- P/U Trk
1- Irrigation truck
1- Cat skid Steer

PANTALEO on Site (one surface crew)

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-12-12

Signed [signature] **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/12/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		
BLAUVELT	KENNETH	PMC			X
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/12/12 TUESDAY WEATHER Sunny/rain pm TEMP: AM 66 PM 70

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Let it grow continue on planting of trees . Continue on paver installation on the southeast island from the canopy (cut pieces)
					Pantaleo 1 Electrician on site working on UG conduit in the canopy island area.
DUMOR					Loading soil material and hauling to stockpile at Gate 1. Utilized 310SJ backhoe for loading.
Super					
OE					PMC adjusted MH's in stage I west of canopy, backfill trenches for light poles 48C,31B,32B & 49C.
Laborer					Grade area west of southwest island from canopy.
PMC	super	1			
	OE	1			
	LF				
	laborer	2			
	trucks	1			
LET IT GROW		6			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
Pantaleo		1			
ANS	technicians				
APGAR	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		12	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Dozer, 1 Bobcat dozer/backhoe

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION CO. INC. ~~Pantelaleo Electric Co.~~ R.S.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Tuesday June 12, 2012

Weather - Partly cloudy - AM 64 degrees - Cloudy PM - Partly cloudy 80 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 1- Box truck 1- bucket truck 1 ton pick up truck

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Work performed - Workers continued to prep the toll booth lanes prior to conduit encasement. Workers cut and threaded nipples and offets for the inground conduits prior to concrete encasement. Conduit stub ups are being tied off and set for toll booths, gate arms, Ticket dispensers, EZ Pass signals and readers, communication conduits, camera conduits running along the ground prepping for in ground junction boxes and concrete placement.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Tuesday 12 June 2012

Signed RICHARD STRIBLING **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

DAILY NARRATIVE

PA 0327 (07-10)

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 1

Weather: (A.M.) Sunny : 63° /(PM) Sunny : 77°

Activity: Continued rough grading @ stage 1. West of proposed canopy plaza
- Removed existing CB
- Adjusted electrical Mlt cover to grade - west of stage 1
- Performed misc. clean up.

(PMC have limited manpower @ P6)

Manpower:	EQP'T
1- Operator	1- Bit UD 310 SJ
2 - Laborer	

Activity 2: LET IT GROW (EWR) Continued the placement of salt splash pavers North and south of exit and entry plaza canopy.
Started tree planting - North of stage 1, and on island - east of lift station.
- All landscaping work on-going.

Landscape architect James Loudon, visited P6, today. Inspected tree planting and planting locations. All acceptable.

Manpower:		EQP'T	
1- Supervisor	5 - Laborer	1- Concrete saw	1- Bob cat skid steer
1- L/F		1- Irrigation Van	1- P/L 500 M
1- Operator		2- Van F-150	1- comb. hoe 4

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 pm

Date 6-11-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/11/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			X
DAMPMAN	DAVE	BERGEN SIGN			X
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/11/12 MONDAY WEATHER Sunny TEMP: AM 66 PM 72

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Let it grow continue on paver installation on the north center islands from the canopy
					Plant trees in stage I
					Delivery of shrubbery, am site visit by PA Architect - James Loudan
					PMC removed milling machine from site. Adjusting and/or abandoning required MH's in Stage I
DUMOR					
Super					Pantaleo - 2 electricians working on underground conduit under canopy
OE					Pantaleo underground labor force not on site
Laborer					Placed concrete for conduit run 48C, 31B, 32B and 49C
PMC	super	1			
	OE	1			Bergen sign arrived at 9am to install missing ground mount STOP signs in stage IIIC
	LF				
	laborer	2			
	trucks	1			
LET IT GROW		7			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen		2			
Mayflower					
Falcon	surveyor				
Pantaleo		2			
ANS	technicians				
APGAR	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		16	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Dozer, 1 Bobcat dozer/backhoe

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0527/07510

Contractor: PAVING MATERIALS AND CONSTRUCTION CO. INC. ~~Pantelaleo Electric Co.~~

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - June 11,2012

Weather - Partly cloudy - AM 64 degrees - Cloudy PM - Partly cloudy 75 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 1- Box truck 1- bucket truck 1 ton pick up truck

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Work performed - Workers finalized the conduit prep work for the toll booth lanes prior to conduit encasement. Offets for the inground conduits were set and adjusted . Conduit stub ups are being tied off and set for toll booths, gate arms, ticket machine, camera's and EZ pass connections. Workers trenching out the addinonal conduits for the toll booth lanes. Additional communication conduits were postioned and aligned for them to land in jubction box. Boxes to be delivered to the site. Concrete arrived and was placed in trench on the east side of P6 parking lot, Manhole enclouser next in front of service building, and around the conduits in the toll booth lanes.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-~~N/A~~ SUB CONTRACTOR POURED APPROX 9 YDS OF CONCRETE TO ENCASE AND FORM DUCTBANK FOR THE POLE LIGHTING CONDUITS

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date 11 June 2012

Signed RONALD STRIBLING

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 /12

Weather: (A.M.) Sunny: 59° /(PM) Sunny: 81°

ACTIVITY: DUMOR CONTRACTING (SUB) Resumed drainage construction on Brewster Rd. Started the excavation of existing pavement @ the location of CB#52.

- Dumor modified CB-52, structure due to underground interference (water line and communication line) that interfered with catch basin location.
- After modification. Dumor placed CB 52, and two (2.0) 8"Ø x 6' DIP pipe and tied in to existing CB that has to be converted to MH
- Before the end of workday, Sub-contractor restored the excavated trenches and replaced the concrete barrier.

Note: Work performed today by Dumor will be charged to Net cost item DWG. GC05 GEN. NOTES 11A. REPAIR, REPLACE OR RELOCATION OF UNDERGROUND UTILITIES NOT SHOWN ON THE CONTRACT DRAWINGS.

Manpower:	EQP'T.
1- Supervisor	1-B/H JD 270 LC
1- Operator	1- Close cab Util. trk. F-350
2- Laborer	1- P/U Trk. F-350
	1- Concrete saw

CLASSIFIED ITEM No. 10. BASE COURSE, PER CUBIC YARD. Contractor delivered 0 CYS today to be used for base course.

- Continued proof rolling of existing base South of entry plaza

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM – 3:30 PM

Date 6-8-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE

PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 2 of 2

Weather: (A.M.) Sunny : 59° /(PM) Sunny: 81

Proof rolling found satisfactory.

Total of 103.58 C.Y. have been delivered today.

Manpower:

1- Supervisor	1- Dozzer CAT D5M LGP
1- L/E	1- P/U Trk F-350
1- O	
4- L	

LET IT GROW (SUS) Continued landscaping work North and south of stage 1 & 2

Note: Trees to be planted was delivered today.

- Landscape Architect, James Loudin, visted the site.
- Checked Trees and planting locations. All wer satisfactory.
- Landscaping work on going.

Manpower:

	EQP'T
1- Supervisor	1- JD Min 4 hoe
1- Operator	1- Bob CAT T 300 skid steer
1- L/E	1- P/L 580 M
5- Laborer	2- F 150 VAN
	1- UTL. P/U Trk. F-350
	1- Irrigation Van

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM – 3:30 PM

Date 6-8-12

Signed [signature] **Counter Signed** _____

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/8/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			X
JERRY	DUFFY	DUMOR	2/13/2013		X
MOREIRA	CESAR	DUMOR			X
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			X
COVCEIRO	PAUL	DUMOR			X
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		X
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		X
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		X
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		X
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/08/12 FRIDAY WEATHER Sunny TEMP: AM 62 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PAPD arrived at ~ 8 am for lane closure for Dumor installation of CB 52
					Cut off required length from CB 52 & installed. Installed 2 -8" DIP to converted existing CB to MDH 53.
					Let IT Grow continue with paver installation on the north center island
					Grading soil along Brewster Road in Stage I
DUMOR					Continue on irrigation piping in northeast island from canopy
Super		1			Delivery of trees (Elm & Lilac) PA Architect Jim Loudan on site at 10:15 am, left at 11am. Found trees
OE		1			delivered to be acceptable
Laborer		2	1		
PMC	super	1			Pantaleo fixed lights at Bus Shelter # 9
	OE	2			
	LF	1			PMC grading DGABC south of canopy
	laborer	5	1		DGABC deliveries
	trucks				Delivery of 4 yellow prows
LET IT GROW		9			
Bamco					Falcon survey on site in pm
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor	1			
Pantaleo		2			
ANS	technicians				
APGAR	sweeper				
Berto	CF,CARP,IW				
TOTAL:		25	2		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Dozer, 1 Bobcat dozer/backhoe Dumor 2 F350 p/u, utilixze 270LC BH

Bamco - 1 6042 Skytrak forklift #N59463

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION CO. INC. ~~Pantelaleo Electric Co.~~ R.S.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - June 08, 2012

Weather - Partly cloudy - AM 64 degrees - Cloudy PM - Partly cloudy 80 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 1- Box truck 1- bucket truck 1 ton pick up truck

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC

Work performed - Workers continued to prep the toll booth lanes prior to conduit encasement. Workers cut and threaded nipples and offets for the inground conduits prior to concrete encasement. Conduit stub ups are being tied off and set for toll booths, gate arms, ticket machine, camera's and EZ pass connections. Pantalaeo contiuned the repair of lights not working in bus station # 9. Workers tested circuits and fuses form sidewalk junction box to the shelter and found a short circuit in the line. Workers removed the light fixture, removed the conductors from the light fixture back down to the home run connection. Removed Conductors had cuts and burns from being puntured through the sheetmetal behind the fixture. Wokers replaced existing conductors and reinstalled light fixture.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - Pantalaeo will be billing PMC for 4 hours plus materail for the repair to bus sheltor #9 lighting. PMC assembled and installed the lighting and the conductors for the bus sheltor and Pantaleo connected the homeruns circuits at the base of the bus sheltor. The Port Authority paid for a working bus sheltor and should not be liable for this repair.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date 08 June 2012

Signed RONALD STRIBLING **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. /

Weather: (A.M.) Sunny : 55° /(PM) Sunny : 75°

(Note) Spent most half a day for KIOSK training FAR PART 169 for ID renewal.

PMC (sub) Continued rough grading @ area located North and South of entry/exit plaza, Grading on going.

CLASSIFIED ITEM No 10. Base Course, per cubic yard.

Contractor delivered DGABC today to be used for base.

Total of 191.38 CY have been delivered.

191.48 w/ pmc tch

Manpower:	EQP'T
1- Supervisor	1- Dozzer Cat D5M LGP
1- Operator	1- Roller Cat CB 778
6- Laborer	2- P/U Trk F-350

LET IT GROW (SUB) Continued the placement of salt splash pavers North and south of proposed entry/exit plaza.

- All landscaping work by Let It grow on going.

Manpower:	EQP'T
1- Supervisor	1- Bob CAT T 300 skid steer
1- L/F	1- P/L 580 M
1- Operator	2 F-150 Van
5- Laborers	1- Irrigation Van
(PANTALEO On site)	1- Concrete saw
2- surface crew	

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM – 3:30 PM

Date 6-7-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/07/12 THURSDAY WEATHER Sunny TEMP: AM 63 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC excavating asphalt for Pantaleo Electric underground in Stage I
					Installed DGABC on entrance to canopy.
					Let it grow continue on paver installation on the se island from the canopy
DUMOR					Worked on the irrigation piping system by the hot-box
Super					
OE					Falcon survey on site in pm
Laborer					
PMC	super	1			DGABC deliveries throughout afternoon
	OE	2			
	LF				PA Materials Tom Murphy picked up sample of DGABC in am for testing.
	laborer	4			
	trucks				
LET IT GROW		7			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor	1			
Pantaleo		2			
ANS	technicians				
APGAR	sweeper				
Berto	CF,CARP,IW				
TOTAL:		17	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Dozer, 1 Bobcat dozer/backhoe

Bamco - 1 6042 Skytrak forklift #N59463

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: ~~Pantelaleo Electric Co.~~ PAVING MATERIALS AND CONSTRUCTION CO. INC. R.S.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - June 07, 2012

Weather - Partly cloudy - AM 64 degrees - Cloudy PM - Clear 79 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 1- 1 ton pick up truck

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Work performed - Workers continued to prep the toll booth lanes prior to conduit encasement. Workers cut and threaded nipples and offets prior to concrete encasement. Conduit stub ups are being tied off and set for toll booths, gate arms, ticket machine, camera's and EZ pass connections. Pantalaeo responded to report of lights not working in bus station # 9. Workers tested circuits and fuses form sidewalk junction box to the shelter and found a short circuit in the line.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - None

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date 07 June 2012

Signed RONALD STRIBLING **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 2

Weather: (A.M.) Sunny : 54° /(PM) Sunny : 72°

Asphalt (PMC) continued saw cutting and removal of existing pavement for kerf located west of Stage 1
- Loaded out debris from site.
- Also continued grading north of proposed entry / exit plaza.
- Performed miscellaneous clean up.
(Note: Contractor relocated construction trailer)
All work on going @ Stage 1.

Manpower:	EQP'T.
1- Supervisor	1- B/H 310 SJ
1- L/F	1- Concrete saw target pro 11
4- Laborer	2- P/U Trk. F-350
	1- D/Trk.

LET IT GROW (SUB) Continued the placement of soil splash pavers and top soil @ various locations @ proposed landscape area.
- All work on going.

Manpower:	EQP'T.	
1- L/F	1- P/Loader	2- Van F-150 Service truck
2- operator	1- Concrete saw	1- P/U Trk.
5- Laborer		

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM – 3:30 PM

Date 6 – 6 – 12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 2 / 2

Weather: (A.M.) Sunny : 54° /(PM) Sunny : 72°

Misc.

Mr. Shane Byrne, Alex Gilowitz and Mathew Mcardale from Hampton clarke picked up sample of materials stockpiled @ south end.

- Notified Landscape Architect, James Lauton about the trees that have to be planted @ P6.
- Pantaleo surface crew on site.
- ISAMCO - removed the initial wall panel @ service bldg. due to not approve wrap.
- ISERTO Not on site.

CLASSIFIED ITEM No. 10. BASE COURSE, PER SQ. YD.

Contractor delivered DGABC for Base today.

Total of 12.17 CY. have been delivered.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6 - 6 - 12

Signed [signature] **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/06/12 WEDNESDAY WEATHER Sunny TEMP: AM 55 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Bamco removed wall panels installed yesterday. Building wrap came back NA and stainless screws were not being used as per Bamco shop drawing dated 4/5/12 &spec section 07419-5 and 8. Bamco left at 10 am.
					PMC worked on excavation for underground conduit in stage I west. Conduit install by Pantaleo Till area along Brewster Road for LIG compost. Grade area north of canopy in pm.
DUMOR					Let it grow continue with paver installation in southeast island south of canopy. Install compost along sidewalk along Brewster Road in Stage I
Super					
OE					
Laborer					Bamco has 13 crates of wall panels on site.
PMC	super	1			
	OE	2			Two storage trailers removed from site.
	LF	1			
	laborer	3			
	trucks	1			
LET IT GROW		5			
Bamco		1			
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
Pantaleo		2			
ANS	technicians				
APGAR	sweeper				
Berto	CF,CARP,IW				
TOTAL:		16	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Dozer, 1 Bobcat dozer/backhoe

Bamco 1 p/u + 1 6042 Skytrak forklift #N59463

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE

PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. /

Weather: (A.M.) 58 /(PM) 64

Activity: (PMC) Performed saw cutting of existing pavement @ Stage 1, in preparation of pavement removal for Kerf and placement. of pvc conduit for light poles (west of entry/exit plaza)

-Also started the rough grading @ area North of proposed entry /exit plaza canopy.

-Performed clean up and removal of debris between existing sidewalk and salt splash paver- north of Stage 2.

-All work on going.

Manpower:	Equipment
1-Supervisor	1- Conrete saw
1-L/F	1- B/H 310 SJ JD
1-Operator	2- P/U Trk. F-350
5- Laborer	

Let It Grow (Sub) Continued the placement of salt splash pavers @area located east of existing lift station and south of entry/exit plaza.

Also continued the spreading of top soil @ proposed landscape area @various locations- North of Stage 2.

-All lanscaping work on going.

Manpwer:	Eqpt.
1-L/F	1- P/L Loader Komatsu
2-Operator	1- Concrete saw
5 Laborer	2- Service Van F-150

Pantaleo on site (surface crew-2 manpower)

Bamco on site (stared working @ sevice blding)

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 A.M. - 3:30 PM

Date 6-5 12

Signed _____ **Counter Signed** _____

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/05/12 TUESDAY WEATHER Sunny TEMP: AM 52 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					9am Progress Meeting at Building 80
					PMC install Green Guard Ultra Wrap on Service Building, PMC advised of no status on submittal, just went in on 5/31. M. Whitehead mentioned submittal as per spec in progress meeting.
					Grading north of canopy
					Sawcut pavement west of canopy for Underground electric work
DUMOR					
Super					Berto 2 laborers on site rubbing concrete barrier east and west of the canopy, left at 1 pm.
OE					
Laborer					Let it grow install irrigation at the sw island from the canopy, continue paver installation
PMC	super	1			Continue on DGA on north center island, ANS on site for testing
	OE	2			Grading compost south of the crossover area.
	LF	1			
	laborer	3	I		Bamco 1 super, 1 CF, 1 Carp start wall panel installation on service building west side
	trucks				
LET IT GROW		8			It was mentioned in the progress meeting that lack of the lightning protection submission impacts the
Bamco		3			ground grid surrounding the canopy & service building. Additional submittal on ceiling hanger supports
CONSOLIDATED					to be supplied by Bamco as indicated by PMC.
Trematore	plumber				
Straight Edge					PMC moved their field trailer to Stage IIIC
Bergen					
Mayflower					ANS & PA Materials checked DGABC on the north center island from canopy.....OK
Falcon	surveyor				
ANS	technicians	1			
APGAR	sweeper				
Berto	CF,CARP,IW	2			
TOTAL:		21	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Dozer

Berto 1 p/u truck Bamco 1 p/u + 1 6042 Skytrak forklift #N59463

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1&2,3) Sht. 1 / 1

Weather: (A.M.) Rainy : 69° /(PM) Rainy : 76°

Note: Due to rainy condition, Contractor performed limited work today.
- Started the initial grading @ stage 3D (North of P6)
- Grading on going.

Manpower: EQP'T.
1- Supervisor 1- B/H JD 270 LC
1- Operator

LET IT GROW (SUB) Continued the placement of salt splash pavers @ area east of existing lift station.
- Due to heavy rains. Let it grow left the site early.
- Installation of pavers on going.
- Also continued the application of top soil @ landscape area North of Stage 2.

Manpower: EQP'T.
1-L/F 1- Concrete saw
5-Laborers 2- Service F-150
1-operator 1- Dozer

ISERTO CONSTRUCTION on site (left early due to rainy condition).

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00AM - 3:30 PM

Date 6-4-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/5/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			X
LABOR	LUIS	BERTO			X
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		X
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		X
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
MEYER	STEPHEN	LET IT GROW	5/10/2015		X
SOTO	TONY	LET IT GROW	5/14/2015		X
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		X
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		X
MARCO	MIRASSOL	LET IT GROW	2/8/2015		X
AQUINO	RICHARDS	BAMCO	11/30/2012		X
MARTINEZ	FERNANDO	BAMCO	TEMP		X
POPIELARSKI	ROBERT	BAMCO	TEMP		X

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/04/12 MONDAY WEATHER RAIN/Cloudy TEMP: AM 61 PM 60

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Berto - remove formwork from barrier curbs under canopy, chip excess concrete by west barrier, left 10:30
					LIG continue on paver installation on south islands from canopy, crew except for twp left at 9 am
					PMC attempt to sawcut for electrical underground work in stage I west of canopy
DUMOR					No Pantaleo underground crew on site. Two electricians working on underground conduit under canopy.
Super					
OE					Limited to no activity due to heavy rain PMC field crew except for OE left in am.
Laborer					
PMC	super	1			Two Pantaleo electricians working on conduit in canopy islands
	OE	2			
	LF	1			
	laborer	3	1		
	trucks				
LET IT GROW		5			
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
ANS	technicians				
APGAR	sweeper				
Berto	CF,CARP,IW	4			
TOTAL:		16	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Bobcat tiller

Berto 1 utility truck, 1 p/u

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION CO. INC ~~Pantelaleo Electric Co.~~

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - June 04, 2012

Weather - Partly cloudy - AM 64 degrees - Cloudy PM 72 degrees - Rain

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 1- 1 ton pick up truck

Subcontractors on site- ~~None~~ PANTALEO ELEC. CO.

Work performed - Workers continued to prep the toll booth lanes prior to conduit encasement. Workers cut and threaded nipples and offets prior to concrete encasement. Conduit stub ups are being tied off and set for toll booths, gate arms, ticket machine, camera's and EZ pass connections.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - None

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date 04 June 2012

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1&2,3) Sht. 1 /

Weather: (A.M.) Sunny : 68° /(PM) Sunny : 75°

PAVING surface crew on site

ACTIVITY : CLASSIFIED (work) ITEM No. 4: REMOVE CONCRETE SIDEWALK OR CONCRETE ISLANDS, PER SQ. YARD.

- Contractor completed the removal of existing sidewalk located North of Stage 3D (P6), south east of Brewster Road
- Also continued the loading out of concrete debris.
- Total of 570' x 7' of sidewalk have been removed (representing 443.33 S.Y. (note: Started the removal on : 5/31/12)

Manpower:	EQP't.
1- L/F	1- B/H PC 270 LC JD
1- Operator	1- F/L 644H
1- D/TK Driver	
1- L	

ACTIVITY 2: LET IT GROW (SUS) Continued placement of salt splash pavers east of existing lift station.

- Also continued the placement of irrigation sprinkler heads North of Stage 1A
- Also performed clean up.
- Placement of irrigation sleeve and pavers on going.

Manpower : 1-L/F , 1-Operator , 3-Laborer EQP't. 1-B/H Komatsu ; 1-Van F-150

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00 AM — 3:30 PM

Date 6-01-'12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/01/12 FRIDAY WEATHER Sunny TEMP: AM 61 PM 70

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					BERTO Placed 9 cy of Cat V concrete for barrier curb on the east side of Lane 7 and the west side of Lane 1. PA Mareials Alfredo Coelho was on site Air 5.5% w/c .421
					Let It Grow install irrigation heads at the southeast island from the canopy. Continue paver installation on the south center islands from the canopy (cut pieces)
					Install DGABC in the north center island from the canopy
DUMOR					
Super					PMC grading landscape area in the NW quad of stage I. Clean up/removals in stage IIID
OE					Grade southwest island from canopy
Laborer					
PMC	super	1			
	OE	2			
	LF	1			
	laborer	3	1		
	trucks	1			
LET IT GROW		5			
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
ANS	technicians				
APGAR	sweeper				
Berto	CF,CARP,IW	4			
TOTAL:		17	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

LIG 1 van , 1 Komatsu Loader, 1 Bobcat tiller

Berto 1 utility truck, 1 p/u

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. /

Weather: (A.M.) Sunny. /(PM) Sunny.

ACTIVITY : PMC - Performed clean up @ Stage 2 - North east in preparation of turning over additional parking spaces to the facility.

- At around 9:00 AM today, A walk-through were performed for Partial/ Final Inspection
- Punch list was generated and submitted to the office engr. Mr. Bob Hollman same with the attendance report.
- Before the end of the day, today. Stage 2 - North east opened up.
- Temporary mounted signs were all up.

MP (PMC)	EQP'T
1- Supervisor	1- BA 810 SU JD
1- L/F	2- P/U Trk F-350
2- L	

CLASSIFIED ITEM No 11 PLANT MIX PER TON. Contractor laid and paved 21.0 Tons of PMM @ area located south of entry / exit plaza.

Manpower	EQP'T
1- L/F	1- Roller SW 500
2- Laborer	1- Plate tamper
	2- P/U Trk. F-350

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00 AM - 3:30 PM

Date 6-29-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 of 1

Weather: (A.M.) Rainy : 72°

/(PM) Cloudy / 70

Note : Due to thunderstorm @ the early part of the day Contractor performed limited work.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM –

Date 6-25-12

Signed _____ **Counter Signed** _____

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/29/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			X
ESTEVES	DANIEL	BERTO			X
PEREIRA	VELSON	BERTO			X
FERREIRA	JORGE	BERTO			X
LABOR	LUIS	BERTO			X
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	7/27/2012		X
PURRELLI	RAYMOND	PANTALEO	7/17/2012		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			X
LAWLOR	PAT	RCC			X
BERNARDI	MIKE	RCC			X
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		X
LAGANELLA	TONY	PMC	8/10/2012		
MADRIGAL	ANTONIO	PMC	**5/12/2012**		X
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		
MEYER	STEPHEN	LET IT GROW	5/10/2015		
SOTO	TONY	LET IT GROW	5/14/2015		
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		
MARCO	MIRASSOL	LET IT GROW	2/8/2015		
LOPEZ	MARCO	LET IT GROW	TEMP		
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

DAILY NARRATIVE

PA 0327 / 05-10

Contractor: Paving Materials and Construction Co. Inc.

Contract Number: EWR 154.028 Rehabilitation of Parking Lot P6 and Gas Station Site

Location: North East and Northwest side of the P6 Parking lot

Date - Friday June 29, 2012

Weather - AM was Partly cloudy - 79 degrees - PM was partly cloudy about 98 degrees - Humid

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: Pantaleo Electric had 1 - Box truck 1- bucket truck 1 ton pick up truck

Subcontractors on site- Pantaleo Electric Inc.

Pantaleo workers set another pole on new base and connected the wiring from the previously pulled home run lighting circuits to (3) new pole bases.

Verified the camera conduit running to pole 18A per the RFI

Pantaleo workers cleaned and organised their "C" Container and truck.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - Verizon Subcontrators were on site repairing the bases of their existing manhole structures along Brewster road.. Workers rebricked the top portion of structures and set new collars and lids.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Friday 29 June 2012

Signed RONALD STRIBLING

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/29/12 Friday WEATHER Sunny TEMP: AM 73 PM 97

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC excavate footings for ground mount signs in Stage 1 east
					Placed plant mix at the south canopy islands to ramp down equipment
					Opened up stage 1 east in pm
					BERTO excavated, placed rebar and placed 7 cy of concrete for the exit lane Prow foundations
					PA Materials Felipe Toussaint on site 4% air
DUMOR					One single bollard shown on drawing A103 was removed to accommodate Prow in island #5
Super					2 pm start excavate for manual exit gate footings with 50d backhoe
OE					RRC start on the south cornice angles in the sw corner . Continue welding the south canopy angle to box
Laborer					girder 19 cornice angles tacked in place from the sw corner
PMC	super	1			
	OE	1			
	LF	1			Let It Grow on site at noon for water planting
	laborer	2			
	trucks				
LET IT GROW		1			
Bamco					
CONSOLIDATED					Partial Final Inspection was held for Stage 1 east (west of the canopy) at 9am by C. Hernandez
Trematore	plumber				
Straight Edge					Verizon site visit in am regarding resetting their two HH covers on East Brewster Road. JFC arrived in pm to
Bergen					reset covers
Mayflower					
Falcon	surveyor				
RRC	welder/laborer	3			9 am meeting with WO # 49 in Building 80
ANS	technicians				
Apgar	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,OE,IW,Lab	5			
TOTAL:		14	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

RRC 2 manlift, 1 F250 p/u 2 Lincoln welder outback 185 & Ranger 8

Berto Mason Dump F550, 1- 50D BH, 1 3500 P/U

ADDITIONAL COMMENTS / DIRECTIVES:

The PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 2

Weather: (A.M.) Sunny : 73° /(PM) (PM) Sunny : 91°

ACTIVITY · STRAIGHT EDGE STRIPING (SUB) On site today and performe striping of new parking spaces @ Stage 2 - North east of P6 / adjacent - west of new entry exit plaza.
- Also installed plastic car bumpers - east of stage 2
- Straight able to complete the striping today

Manpower :	EQP'T.
1 - F	2 - Thermo truck
3 - Laborer	2 - Striping Machine
	1 - Compressor

ACTIVITY 2: BERGEN SIGNS (SUB) was on site today and continued the installation of isle marker sign @ stage 2 - North east (adjacent - west of entry / exit plaza
- Installation not complete. BERGEN signs has to come back for the placement of ground mounted sign.

Manpower :	EQP't.
2 - Laborer	2 - Boom truck

Activity 3: (PMC) Performed saw cutting of existing pavement (stage 2 - N/east)

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00 AM - 3:30 PM

Date 6-28-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327/07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 2 / 2

Weather: (A.M.) Sunny: 73° /(PM) Sunny 91°

for the placement of ground mounted sign footings.
Saw cutting and excavation not complete, Will continue next day.

Manpower:	EQP'T
1- Supervisor	1- Bkt JD 310 SJ
1- Operator	1- Compressor
2- Laborer	1- Jack hammer
	1- Concrete saw
	2- P/U Trk. F-350

RCC on site welding work @ canopy plaza.
Pantaleo Electric - surface / sub surface crew on site.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00AM - 3:30PM

Date 6-28-12

Signed [signature] **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/28/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			X
RIVAS	JOSE. M	STRIAGHT EDGE			X
VIDES	JUAN. C	STRIAGHT EDGE			X
VIDES	JOSE. H	STRIAGHT EDGE			X
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	7/17/2012		X
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		X
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			X
LAWLOR	PAT	RCC			X
BERNARDI	MIKE	RCC			X
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		
DUARTA	VICTOR	PMC	**5/23/2012**		X
LAGANELLA	TONY	PMC	8/10/2012		
MADRIGAL	ANTONIO	PMC	**5/12/2012**		X
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		
GREEN	WILLY	PMC	4/26/2015		
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			X
DAMPMAN	DAVE	BERGEN SIGN			X
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		
MEYER	STEPHEN	LET IT GROW	5/10/2015		
SOTO	TONY	LET IT GROW	5/14/2015		
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		
MARCO	MIRASSOL	LET IT GROW	2/8/2015		
LOPEZ	MARCO	LET IT GROW	TEMP		
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/28/12 Thursday WEATHER Sunny TEMP: AM 71 PM 91

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					RRC continue on cornice support angle welding on the north side 34 pieces in place - 19 - yesterday
					All in place on the north side by days end
					PA Materials Lance Krakovitch visited the site in late am. One welder in site in am.
					PMC excavating for ground mount fdn's north of canopy & stage 1D
DUMOR					Straight Edge striped stage 1D (west of canopy)
Super					Start bumper installation in the SE corner of stage 1D
OE					
Laborer					Bergen Sign arrived at 9am for light pole signage in stage 1D
PMC	super	1			
	OE	1			Gate arm delivery in am for plaza
	LF	1			
	laborer	2			Let it grow on site for watering in pm.
	trucks				
LET IT GROW		1			PA Materials notified of tomorrow's 12:30 concrete placement by Berto
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge		4			
Bergen		2			Pantaleo Underground crew return to work on east end of stage 3D.
Mayflower					Removed old light poles in stage 3D along with fdn's
Falcon	surveyor				
RRC		2			
ANS	technicians				
Apgar	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		14	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

RRC 2 manlift, 1 F250 p/u 2 Lincoln welder outback 185 & Ranger 8

ADDITIONAL COMMENTS / DIRECTIVES:

Contractor: Paving Materials and Construction Co., Inc.

Contract Number: EWR 154.028 Rehabilitation of Parking Lot P6

Location: Parking Lot P6 on Brewster Road

Ambient Temperature: AM 71° PM 90° Weather Conditions: Sunny

Activity 1: PMC excavation of ground mounted sign footings

Man Power: Laborers: 2

Operators: 1

Equipment: Tractor hoe (Deere 310SJ), Air compressor (#56), jackhammer

Activity 2: Straight Edge Line Stripers striping parking spaces for STAGE 2.

Man Power: Laborers: 1

Foreman: 1

Equipment: Striping Truck (Hino 268)

Activity 3: Bergen Sign installing row/isle identification signs (4), stop signs (4), handicap signs (4)

Man Power: Laborers: 2

Equipment: 2 trucks with lifts

Pantaleo using PMC tractor hoe (Deere 310SE) to excavate duck dank

Swing arms for toll booth delivered at 8:30AM

Idle Machines: Hypac C778B vib. roller, Sakai SW500 vib. roller, Blaw Knox PE5510 paver, CAT AP1055D paver

Wirtgen W2200 milling machine, Hamm HD120 vib. roller, CAT D5M bulldozer, Komatsu WA250 front-loader

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 7:00AM - 3:00 PM

Date June 28, 2012

Signed Jordan Cohen

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/27/12 Wednesday WEATHER Sunny TEMP: AM 65 PM 84

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC paved repair area in Stage 1D. 168' long x 28' wide north-northwest of light pole fdn 65D
					PA Materials E.Dumalog on site ANS tech on site
					Placed 73.05 tons of WMA Completed by 9am
					Two rollers sakai SW 500 + Cat CB 534D utilized along with AP1055D paver
					Excavate for UG conduit runs to light poles (25A) in stage 3D and ground mount sign fdn's south of canopy
DUMOR					RRC Additional welder Mike Berardi AWS # 1090159, exp 4/26/13, SMAW -A1 started today
Super					9am additional manlift delivered
OE					Lance Krakovitch of PA Materials notified of new welder on site.
Laborer					Continue welding cornice support brackets on the north side (15 welded yesterday)
PMC	super	1			Delivered additional angle iron and Lincoln Welder (Ranger 8)
	OE	2			Continue welding angle iron on the south side of canopy
	LF	2			
	laborer	5	1		
	trucks	3			PMC indicated BAMCO & BERTO to come back on Monday 7/2/12
LET IT GROW		1			
Bamco					Let it grow on site in the pm for watering. Many plants seem to be turning brown due to lack of water
CONSOLIDATED					
Trematore	plumber				Bergen sign not on site
Straight Edge					
Bergen					10 am site visit by AON
Mayflower					
Falcon	surveyor				
RRC		3			
ANS	technicians	1			
Apgar	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		18	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

RRC 2 manlift, 1 F250 p/u 2 Lincoln welder outback 185 & Ranger 8

ADDITIONAL COMMENTS / DIRECTIVES:

EWR 154.028 PARKING LOT P6		DATE	6/27/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			
CAROLAN	KENNY	RCC			X
LAWLOR	PAT	RCC			X
DEORIO	TONY	MAYFLOWER			

AGOSTINHO	MATIAS	PMC	**9/20/2012**		X
BLAUVELT	KENNETH	PMC			X
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		
DRUDE	RAYMOND	PMC	**10/8/2012**		X
DUARTA	VICTOR	PMC	**5/23/2012**		X
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		
TOMAS	GILBERT	PMC	**10/8/2012**		X
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		X
GREEN	WILLY	PMC	4/26/2015		X
NETO	JOSE	PMC	PENDING		
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		
MEYER	STEPHEN	LET IT GROW	5/10/2015		
SOTO	TONY	LET IT GROW	5/14/2015		
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		
MARCO	MIRASSOL	LET IT GROW	2/8/2015		
LOPEZ	MARCO	LET IT GROW	TEMP		
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE

Contractor: Paving Materials and Construction Co. Inc.

Contract Number: EWR 154.028 Rehabilitation of Parking Lot P6 and Gas Station Site

Location: North East and Northwest side of the P6 Parking lot

Date - Weds June 27, 2012

Weather - AM was Partly cloudy - 69 degrees - PM was partly cloudy about 79 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: Pantaleo Electric had 1 - Box truck 1- bucket truck 1 -1 ton pick up truck

Subcontractors on site- Pantaleo Electric Inc.

Pantaleo workers were given a shutdown of the east side of P6 lot pedistal ligting contactor to splice in homerun circuits and remove the existing pole lighting conductors. Workers cut spliced and tagged new homerun circuits from hanholes to the Manholes. Workers installed the approved cold shrink wrap to join the feeder circuits to the pole lighting homerun circuits and tagged them with the brass tags for future refrences Workers obtained their confined space permit, set up tripod, barrier, ventaltion, and sniffer prior to. entering manhole. Workers disconnected existing pole lights and pulled conductors completely out from the manhole.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary -

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Weds 27 June 2012

Signed RONALD STREBLING

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. / /

Weather: (A.M.) Sunny: /(PM) Sunny:

ACTIVITY: (Note) First thing in the morning today. Contractor performed milling of previously paved asphalt pavement. Located west of new entry / exit plaza.

- Milling was performed to rectify the water ponding.
- Area milled measured - 62' x 29'
- utilized mobile sweeper to clean up milled area.
- Milled area scheduled to be paved tomorrow.

Manpower:	EQP'T
1 - Supervisor	1 - Milling Machine
1 - L/F	2 - D/Trk
1 - L	1 - P/U Trk F-35
1 - O	

ACTIVITY 2: Continued rough grading @ Stage 3 - North

- Installed Oura art stone bollard parking bollard @ stage 2 - South,
- Continued the clean up
- All work on going.

Manpower		EQP'T
1 - O	2 - Labore	1 - B/H Combination 310 SJ
1 - L/F		2 - P/U Trk F-350

ROC on site - pantalec on site.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-26-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/26/12 Tuesday WEATHER Sunny TEMP: AM 60 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC milled and swept low repaired area in stage 1D
					Start installing dura stone sign post bollards in stage 2 (punch-list item)
					Area that was milled was swept clean and tack coat applied
DUMOR					RRC welding support roof angle on the south side of the box girder canopy
Super					Start welding cornice support steel in the nw corner
OE					
Laborer					
PMC	super	1			
	OE	2			
	LF	1			
	laborer	1			
	trucks	1			
LET IT GROW					
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
RRC		2			
ANS	technicians				
Apgar	sweeper	1			Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		9	0		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

RRC 1 manlift, 1 F250 p/u 1 Lincoln welder outback 185

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE

Contractor: ~~Pantaleo Electric, Inc.~~ PAVING AND MATERIALS AND CONSTRUCTION INC.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Monday June 25, 2012

Weather - AM was Partly cloudy scattered rain - 69 degrees - PM was cloudy with scattered rain 79 degrees

Shift - Day shift

Labor on site - 1 foreman 1 Journeman Electrician

Equipment on site: 1 - Box truck 1- bucket truck 1 -1 ton pick up truck

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Pantaleo workers were given their shutdown of the west pedistal ligting contactor to splice in homerun circuits for light pole's on the west side of P6 lot. Workers cut spliced and tagged new homerun circuits from the existing hanholes to the new pole lighting HH. Workers installed the approved cold shrink wrap to join the feeder circuits to the pole lighting homerun circuits and tagged them with the brass tags for future refrences.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary -

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Monday 25 June 2012

Signed RONALD STRIBLING

Counter Signed

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/25/12 Monday WEATHER Cloudy/rain/sunny TEMP: AM 73 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Lightning at 8am, sporadic rain
					RRC resume angle welding on canopy (north side)
					9:15 delivery of cornice steel
DUMOR					PMC clean up in stage IIID
Super					Investigated pavement low spots in stage 1D
OE					Area in stage 1D (low area) will be milled/paved
Laborer					
PMC	super	1			
	OE	1			
	LF	1			
	laborer	2	1		
	trucks				
LET IT GROW					
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
RRC		2			
ANS	technicians				
Apgar	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		7	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

RRC 1 manlift, 1 F250 p/u 1 Lincoln welder outback 185

ADDITIONAL COMMENTS / DIRECTIVES:

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 /

Weather: (A.M.) Sunny : 72° /(PM) Sunny : 95°

ACTIVITY (NET COST) DWG. G005, GEN. NOTES 11 E - TRANSPORTATION OF SOIL FROM SITE TO STOCKPILE AREA.

Today, PMC resumed hauling out of excess excavated material from site to stockpile area @ Gate 1.

- Hauling out of material on going.

Manpower:	EQPT
1- Operator	1- B/H FC 270 LC
2- D/Trk. Driver	2- Dump trk.

Activity 2: (PMC) started the initial grading North of stage 3, North

- Loaded out concrete debris.
- Performed clean up
- Resumed working @ proposed service building

All work @ service building and grading on going.

Manpower:	EQPT.
1- Operator	1- Combination hoe JD 310 SJ
1- L/F	2- P/U Trk F-350
1- L	

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00 AM - 3:30 PM

Date 6-22-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/22/12 Friday WEATHER Sunny TEMP: AM 83 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					Morning hours at MF100.509 & MFA134.308
					Installed TYVEK on the service building
					Removing material to the Gate 1 area
					Bergen Sign arrived at 10:45 to install sign poles 815 a,b,c,d in stage 2 & light pole signage in stage 1D
DUMOR					
Super					LET IT GROW on site in pm for watering
OE					
Laborer					
PMC	super	1			
	OE	1			
	LF	1			
	laborer	3	1		
	trucks	2			
LET IT GROW		1			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen		2			
Mayflower					
Falcon	surveyor				
RRC					
ANS	technicians				
Apgar	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		11	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

ADDITIONAL COMMENTS / DIRECTIVES:

The PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC.

Contract Number: EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. / /

Weather: (A.M.) Sunny : 73° /(PM) Sunny : 97°

ACTIVITY: (PMC) CLASSIFIED ITEM # 7 - WARM MIX ASPHALT CONCRETE PG 64-22 PER TON.

- Contractor continued Asphalt paving work @ Stage 1D - WEST OF entry / exit plaza.
- Total of 1884.86 Tons have been laid and paved today

Mr. Erick Dunaley from PA QA was on site during paving operation

Manpower:	EQP'T
1- Supervisor	1- Asphalt paver
3- Operator	1- Roller CAT CB 534D
1- Paving Foreman	1- Plate tamper
1- L/F	1- Roller SW-500
5- Laborer	2- Utility P/u Trk.

PANTALEO Surface / sub surface crew on site.

RCC on site

LET IT GROW (Landscaping Contractor) showed up late afternoon @ site watering the plants and shrubs.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00 AM - 4:00 PM

Date 6-21-12

Signed [signature] Counter Signed [signature]

Use form PA 316 to note labor, material or equipment usage.

AGOSTINHO	MATIAS	PMC	**9/20/2012**		
BLAUVELT	KENNETH	PMC			
CARDOSO	DOMINGOS	PMC	**8/16/2012**		X
GUARDADO	DOAQUIN	PMC	**PENDING**		X
DAROCHA	JOSE	PMC	8/9/2012		X
DRUDE	RAYMOND	PMC	**10/8/2012**		X
DUARTA	VICTOR	PMC	**5/23/2012**		X
LAGANELLA	TONY	PMC	8/10/2012		X
MADRIGAL	ANTONIO	PMC	**5/12/2012**		
OXENREIDER	MELVIN	PMC	**10/8/2012**		X
SOPER	RANCE	PMC	**10/7/2012**		X
TOMAS	GILBERT	PMC	**10/8/2012**		X
WHITEHEAD	MICHAEL	PMC	**10/5/2011**		
LASALA	BILL	PMC	8/14/2012		X
GREEN	WILLY	PMC	4/26/2015		X
NETO	JOSE	PMC	PENDING		X
ALVES	ARMANDO	BERTO			
CRISTRANO	AMILCAR	BERTO	**5/24/2012**		
OLIVIERA	ANTONIO	BERTO	**5/24/2012**		
PEREIRA	FERNANDO	BERTO	**5/24/2012**		
MARTINS	JAMIE	BERTO	5/24/2012		
GONZALEZ	LUIS	BERTO	5/24/2012		
BEESLY	RAY	BERGEN SIGN			
DAMPMAN	DAVE	BERGEN SIGN			
FRCELLA	ROBERTR	CONSOLIDATED			
ENRIQUES	JACK	CONSOLIDATED			
ENRIQUES	JOHN	CONSOLIDATED			
MITCHELL	KEVIN	TREMADOR			
LOPEZ	FREDERICO	LET IT GROW	TEMP		
MEYER	STEPHEN	LET IT GROW	5/10/2015		
SOTO	TONY	LET IT GROW	5/14/2015		
MARGARITO	SAQUIL	LET IT GROW	1/18/2013		
ELIAS C.	PAR LOPEZ	LET IT GROW	1/19/2013		
MARCO	MIRASSOL	LET IT GROW	2/8/2015		
LOPEZ	MARCO	LET IT GROW	TEMP		
AQUINO	RICHARDS	BAMCO	11/30/2012		
MARTINEZ	FERNANDO	BAMCO	TEMP		
POPIELARSKI	ROBERT	BAMCO	TEMP		

EWR 154.028 PARKING LOT P6		DATE	6/21/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	7/27/2012		X
PURRELLI	RAYMOND	PANTALEO	7/17/2012		X
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		X
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			X
LAWLOR	PAT	RCC			X
DEORIO	TONY	MAYFLOWER			

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: ~~Pantaleo Electric, Inc.~~ PAVING MATERIALS AND CONSTRUCT CO. INC

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Friday June 22, 2012

Weather - Partly cloudy & Humid - AM 79 degrees - PM - cloudy Humid 98 degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- ~~None~~ PANTALEO ELECTRIC INC.

Pantaleo workers continued splicing in circuits for light pole's from handhole's to pole bases near the service building between the east and west side of P6 lot, and near the gate entrance along Brewster road. Workers installing light pole circuits from new pole bases to new hanholes prior to connections to homerun manholes.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - Verizon workers completed their repair of the broken Verizon ductbank along side electrical ductbank. Verizon workers remained on site to test and slice newly installed fibor lines. Trench containing repair communication ductbank remains open. Contacted Verizon to confirm their comletion and asked if encasement was needed for their Ductbank. Pantaleo clear to backfill trench. Verizon Ground crew will return next week to re brick their Manhole frame and lids.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Friday 22, June 2012

Signed _____ **Counter Signed** _____

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: ~~Pantaleo Electric, Inc.~~ PAVING MATERIALS AND CONSTRUCTION CO. INC

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Thursday June 21, 2012

Weather - Partly cloudy & Humid - AM 79 degrees - PM - Clear Humid 98 degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- ~~TBE~~ PANTALEO ELECTRIC Co.

Pantaleo workers continued pulling in circuits for light pole's from handhole's to pole bases near the service building between the east and west side of P6 lot. Workers installing light pole circuits from new HH and ductbanks to new pole bases previously set. Ground crew workers replaced conduit ductbank removed by Verizon workers repaing broken fiber lines. Pantaleo workers supported and seperated electric ductbank conduits from newly installed communication conduits prior to concrete ecasement. Workers placed concrete and encased electcal conduits from HH to light pole base. From new pole base encased conduit.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - Verizon workers repaied a broken Verizon ductbank and pulled in new fiber lines. along side electrical ductbank. Verizon workers remained on site to test and slice newly installed fibor lines.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Thursday 21 June 2012

Signed _____ **Counter Signed** _____

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/21/12 Thursday WEATHER Sunny/HOT TEMP: AM 83 PM 97

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC paved stage ID (west of canopy)
					RRC start welding misc steel on canopy as per approved submitted drawings 05506-0008 to 0012
					Certified welder Ken Carolane doing the welding
					PA Materials Lance Krakovitch notified of welding activity and visited the site in the late am.
DUMOR					
Super					Discussed with PMC super that it appears the area between the canopy box girder and exterior ceiling
OE					panels, was not addressed as far as covering. Appears the exterior plywood would be exposed. (A204)
Laborer					
PMC	super	1			Received welding inspection reports from RRC from previous canopy welding from March & April/2012
	OE	3			
	LF	2			
	laborer	6	1		
	trucks	9			
LET IT GROW					
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					VERIZON ON SITE SINCE YESTERDAY REPAIRING A DUCTBANK HIT BY PANTALEO ELECTRIC
Bergen					YESTERDAY ON THE EAST END OF BREWSTER ROAD.
Mayflower					
Falcon	surveyor				
RRC		2			
ANS	technicians	1			
Apgar	sweeper				Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		24	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

RRC 1 F250 p/u, 1 Lincoln Welder Outback 185

ADDITIONAL COMMENTS / DIRECTIVES:

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 1 / 2

Weather: (A.M.) Sunny 73° /(PM) Sunny : 87°

ACTIVITY : (PMC) Resumed Asphalt paving operation @ area west of entry / exit plaza (proposed)

- Before asphalt paving occured. Contractor applied tack coat @ areas to be paved.

CLASSIFIED ITEM Nº 8. TACK COAT, PER SQ. YD.

Total of 4,915.55 SY, have been tack coated today (attached sketch of computation sketch 2 of 2).

Manpower :	EQP'T
1- Tack Trk. Driver	1- Tack truck

- After applying tack coat. Contractor resumed paving work. Paving that was performed today was leveling course.

CLASSIFIED ITEM Nº. 7. WARM MIX ASPHALT CONCRETE (PG 64-22) PER Ton.

- Total of 565.27 Tons have been laid and paved today.

Manpower :		EQP'T	
1- Supervisor	4-L	1- Asphalt paver	1- Comb. hoe 310 SG
2- Operator		1- Roller CB 778B	2- P/U Truck
1- Paving Foreman		1- Roller SW-500	
1- L/E		1- Plate tamper	

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00 AM – 4:00 PM

Date 6-20-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

The PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. /

Weather: (A.M.) Sunny : 75° /(PM) Sunny : 97°

CLASSIFIED ITEM No. 10. BASE COURSE, PER SQ. YD.

- Contractor delivered DGABC today for base course.
- Total of 58.03 CY. delivered today.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:00AM – 4:00 PM

Date 6-20-12

Signed [signature] **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. 2 /2

Weather: (A.M.) Sunny : 73° /(PM) Sunny : 97°

Note:

At 3:00 PM today. I was informed by PMC supervisor, Mr. Mel Oxenreider, that Verizon fiber optic cable was hit by sub contractor, Pantaleo Electric while excavating for the placement of PVC conduit pipe, located east of P6.

I immediately notified the ARE, Mr. Lars Blanchard, about the incident.

I also called up the electrical inspector, Mr. Ron Stribling, and asked him if he is aware of the incident. Mr. Ron Stribling, said he was not aware of the incident (that time).

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-20-12

Signed [signature] **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

Work Sheets ..... OF .....

Charito L. Hernandez

REHABILITATION OF PARKING LOT P6
EWR- 154.028

Date:

Weather: (A.M.) /(P.M.)

Activity:
Classified Item No. 8: TACK COAT, PER SQUARE YARD.

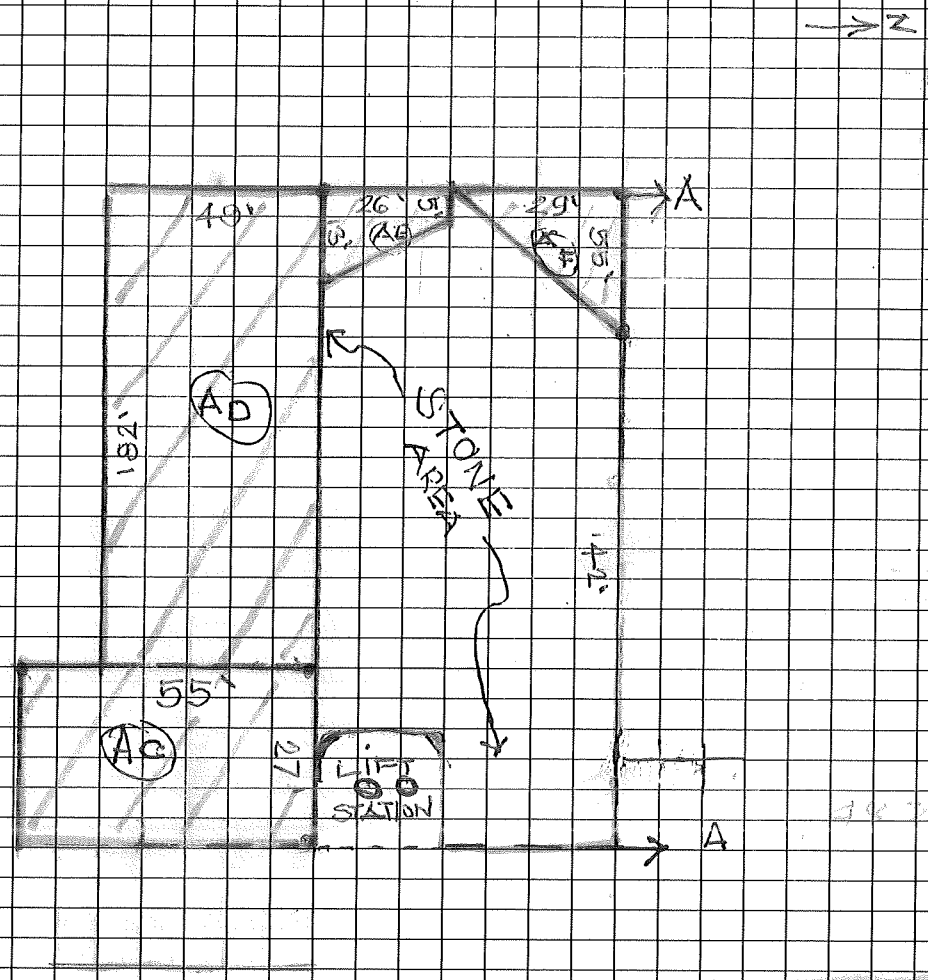

Ac: 55' X 27' = 1,485/9 = 165 SY

AD: 182' X 49' = 8,918/9 = 991.0 SY

AE: $\left(\frac{5' + 13'}{2}\right)$ 26' = 234/9 = 26 SY

AF: (.5) 29' X 55' = 797.5/9 = 88.61 SY

Total Area tack coated:

1,657.61
1,908.00
79.33
1,270.61
= 4,915.55 SY

Areas: Ac + AD + AE + AF

165 + 991 + 26 + 88.61

Area = 1,270.61 SY

Work Sheets 1 OF 1

Charito L. Hernandez

REHABILITATION OF PARKING LOT P6
EWR- 154.028

Date: 6-14-12

Weather: (A.M.) C-57° /(P.M.) S-75

STAGE 1

Activity:
Classified Item No.1:MILL ASPHALT CONCRETE TO 2" BELOW FINISHED GRADE, PER SQUARE YARD

Computations:

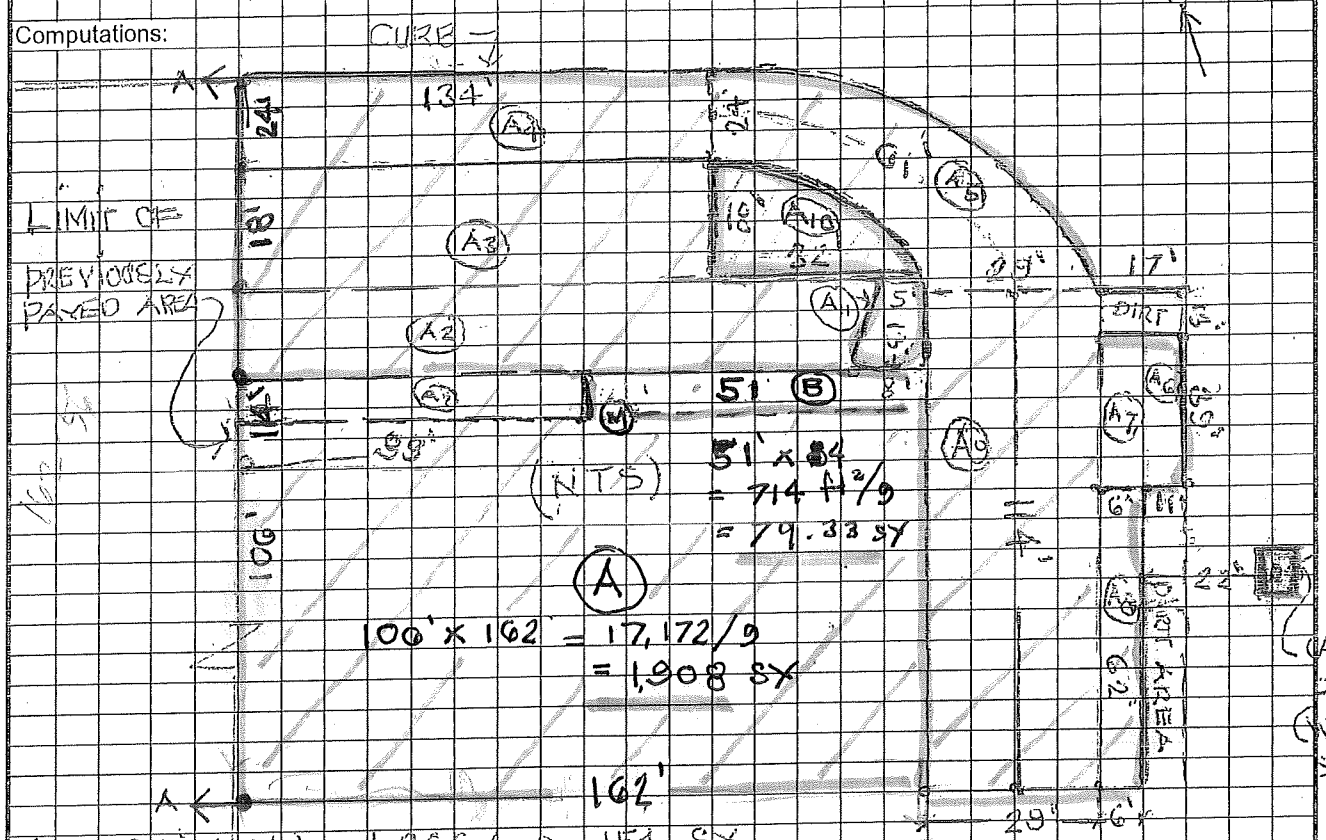

A1: 99' x 14' = 1,386/9 = 154 SY

A2: 150' x 13' = 1,950/9 = 216.67 SY

A3: 134' x 18' = 2,412/9 = 268 SY

A4: 134 x 24' = 3,216/9 = 357.33 SY

A5: $\left(\frac{29+24}{2}\right)$ 61 x 26.5 = 166.5/9 = 179.61 SY

A6: 39' x 11' = 429/9 = 47.67 SY

A7: 39' x 6' = 234/9 = 26 SY

A8: 62' x 6' = 372/9 = 41.33 SY

A9: 114 x 29' = 3306/9 = 367 SY

Area of Island:

A10: (.5) 18' x 32 = 288/9 = 32 SY

A11: $\left(\frac{8+5}{2}\right)$ 13 x 6.5 = 84.5/9 = 9.39 SY

Area of Island: 32 + 9.39 = 41.39 SY

TOTAL AREA MILLED:
A1 to A9
= 1,657.61 SY

LEGEND:
--- Area Milled

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0327 / 07-10

PAVING MATERIALS AND CONSTRUCTION CO. INC.

Contractor: Pantaleo Electric, Inc. **Contract Number:** EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - June 20, 2012

Weather - Partly cloudy & Humid - AM 79 degrees - PM - Clear Humid 98 degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- ~~TBE~~ PANTALEO ELECTRIC INC.

Pantaleo workers continued pulling in circuits for light pole's from handhole's to pole bases near the service building between the east and west side of P6 lot. Workers continued the excavation and trenching for the lighting ductbank along Brewster Rd. Workers installed new pole bases and pulled in home run circuits from pole bases to handhole's.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

Any other information deemed neccarsary - Receivied a call around 2:45 PM regarding a broken Verizon line from Pantaleo's trench along brewster Rd. Upon arrival discovered a broken ductbank and several feet of torn out communication cables. The point of contact from Verizon - Joe Portelli indicated the broken fiber cables shut down the Corbin St. Hut. Interupting service from the Port.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date 20 June 2012

Signed **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/20/12 Wednesday WEATHER Sunny/HOT TEMP: AM 72 PM 94

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC paved leveling course in stage 1D. ANS & PA Materials on site
					Falcon surveyor on site for grade.
					Apgar sweeper on site in pm
					TBE on site for Consolidated Fence Markout, ticket # 121661290 expires 8/17/12
DUMOR					Pantaleo Electric continue on HH and conduit installation on East Brewster Road. Spoke to Mel on
Super					close proximity of duct bank and footings for the ornamental fence.
OE					HH splicing & light pole connections
Laborer					
PMC	super	1			Let it grow arrived in pm to water plants
	OE	2			
	LF	2			Railroad construction delivered manlift in am
	laborer	5	1		
	trucks	6			AON & Chartis site visit in am
LET IT GROW		1			
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor	1			
Pantaleo		6			
ANS	technicians	1			
Apgar	sweeper	1			Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		26	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

ADDITIONAL COMMENTS / DIRECTIVES:

DAILY NARRATIVE PA 0327 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION, CO., INC. **Contract Number:** EWR-154.028

Location: REHABILITATION OF PARKING LOT P6, AND GAS STATION SITE (Stages:1,2&3) Sht. /

Weather: (A.M.) Cloudy : /(PM) Partly sunny

PMC - Continued paving preparation - West of proposed entry / exit plaza. Utilized mobile sweeper for clean up.
- Removed section of previously pavement to create vertical transition.
- Paving preparation completed.

Manpower:	EQPT.
1- Supervisor	1- B/H 310 SJ JD
2- Operator	1- Roller SW-500
1- L/F	1- Plate tamper
3- Laborer	2- P/U utility truck

CLASSIFIED ITEM #11. Plant Mix Macadam, Per ton.
Contractor continued and completed the trench repair and pavement restoration @ areas to be paved.
Total of 25.04 Tons have been used.

Mr. Benny Patel and Mr. Alfredo Coello from ANS-QC and PA QA were on site, tested DGABC for Density - North / south and west of entry / exit plaza. Results are satisfactory.

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift 6:30 AM - 3:30 PM

Date 6-19-12

Signed [signature] **Counter Signed** [signature]

Use form PA 316 to note labor, material or equipment usage.

EWR 154.028 PARKING LOT P6		DATE	6/19/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	**2/13/2013**		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	**7/27/2012**		X
PURRELLI	RAYMOND	PANTALEO	**7/17/2012**		X
SCHANCK	ERIC	PANTALEO	**7/27/2012**		X
SOARES	JOSE	PANTALEO	**11/17/2012**		X
DOEFFINGER	ERIC	PANTALEO	**1/4/2013**		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

EWR 154.028 PARKING LOT P6		DATE	6/19/2012		
LSAT NAME	FIRST NAME	COMPANY	SWAC EXP.		ONSITE
PINTO	JUAN. M	STRIAGHT EDGE			
RIVAS	JOSE. M	STRIAGHT EDGE			
VIDES	JUAN. C	STRIAGHT EDGE			
VIDES	JOSE. H	STRIAGHT EDGE			
BONOMO	ERIN	ARECON			
LaMORTE	MARC	ARECON			
MUNDRAS	CHRISTOPHER J	ARECON			
MUNDRAS	MICHAEL V	ARECON			
PETROSILLI	DARRYL	ARECON			
SMITH	DJ	FALCON SURVEY			
BARROW	JAMES	FALCON SURVEY			
SUTER	ROB	FALCON			
MARQUES	CARLOS	BERTO			
ESTEVES	DANIEL	BERTO			
PEREIRA	VELSON	BERTO			
FERREIRA	JORGE	BERTO			
LABOR	LUIS	BERTO			
SALAZAR	JOSE	DUMOR			
JERRY	DUFFY	DUMOR	2/13/2013		
MOREIRA	CESAR	DUMOR			
PIKE	DOUGLAS	DUMOR	2/13/2013		
RODRIGUES	JOSE	DUMOR			
COVCEIRO	PAUL	DUMOR			
HIEDEL	CHRIS	PANTALEO	7/27/2012		X
PURRELLI	RAYMOND	PANTALEO	7/17/2012		X
SCHANCK	ERIC	PANTALEO	7/27/2012		X
SOARES	JOSE	PANTALEO	11/17/2012		X
DOEFFINGER	ERIC	PANTALEO	1/4/2013		X
KERTESZ	MIKE	PANTALEO			
MELO	JOHN	PANTALEO			X
CAROLAN	KENNY	RCC			
LAWLOR	PAT	RCC			
DEORIO	TONY	MAYFLOWER			

THE PORT AUTHORITY OF NY & NJ

DAILY NARRATIVE PA 0527 / 07-10

Contractor: PAVING MATERIALS AND CONSTRUCTION CO. INC. ~~Pantaleo Electric, Inc.~~ R.S.

Contract Number: EWR 154.028

Location: Rehabilitation of Parking Lot P6 and Gas Station Site

Date - Tuesday June 19, 2012

Weather - AM Temp N/A PM - N/A degrees

Shift - Day shift

Labor on site - 2 foreman 1 Journeman Electrician 1 Operator 2 laborers

Equipment on site: 2 - Box truck 1- bucket truck 2 -1 ton pick up truck 1 Air Compressor 1 Small Dump Truck 1 - Backhoe

Subcontractors on site- None

Pantaleo ground crew workers excavated and trenched approx 95' from HH #1 to HH #2 and installed (2) 2"conduits appox 182' between handholes for new pole lighting duct banks on northeast side of P6

Workers trenched approx. 95' between HH #2 and HH #3 and installed appox, 190' (2) 2" Workers trenched appox 95' from HH #3 to HH #4 and installed appox 190' (2) 2" conduits. Conduits were set on stands and tied down. Concrete was placed to form a ductbank of conduits between the Hand hole structures.

Classified Items Quantities -N/A

T&M Work (extra workand/or net cost work - N/A

Controlled / Special Inspections performed today-N/A

I certify that I have read the applicable paragraphs from the PA Construction Standards manual pertaining to the work/tests described above.

Shift Day

Date Tuesday 19 June 2012

Signed RONALD STRIBLING **Counter Signed**

Use form PA 316 to note labor, material or equipment usage.

DAILY REPORT

URS Construction Manager The Port Authority of NY & NJ	PROJECT: **REHAB OF P6 PARKING LOT** LOCATION: **NEWARK INT'L AIRPORT** INSPECTOR: J.Mihalenko COUNTERSIGNED: DAY	JOB NO.: **EWR 154.028** CONTRACTOR: **PMC** DATE: 6/19/12 Tuesday WEATHER Sunny TEMP: AM 65 PM

CRAFT (LIST ALL CRAFTS)		TOTAL	MINORITY	FEMALE	DESCRIPTION OF DAILY ACTIVITIES
					PMC install plant mix for trench restoration in early am. Grade/clean stage ID west area for paving
					Pantaleo continue with underground conduit for HH's in stage IIID
					Install tremaining light poles in Stage ID
DUMOR					9 am progress meeting at Building 80
Super					
OE					ANS & PA on site toi check DGABC density in Stage ID
Laborer					
PMC	super	1			
	OE	1			
	LF	1			
	laborer	3	1		
	trucks				
LET IT GROW					
Bamco					
CONSOLIDATED					
Trematore	plumber				
Straight Edge					
Bergen					
Mayflower					
Falcon	surveyor				
Pantaleo		6			
ANS	technicians				
ELGIN	sweeper	1			Maser Engineering (2) on site for underground conduit as-builts
Berto	CF,CARP,IW				
TOTAL:		13	1		REFER TO OTHER DAILY REPORTS FOR ADDITIONAL ACTIVITIES , MANPOWER & EQUIPMENT

EQUIPMENT:

ADDITIONAL COMMENTS / DIRECTIVES:
